

Oracle  
**Primavera P6 EPPM**  
**Reporting Guide**

**Version 26**  
January 2026

Oracle Primavera P6 EPPM Reporting Guide

Copyright © 2018, 2026, Oracle and/or its affiliates.

Primary Author: Oracle Corporation

# Contents

---

## About This Guide

---

### Scope

This guide contains information about reports in P6 EPPM including the sample reports provided, the publication services which provide data for reporting and table auditing.

### Audience

Administrators and anyone who creates reports in P6 EPPM should read this guide.

## About Personal Information

---

Personal information (PI) is any piece of data which can be used on its own or with other information to identify, contact or locate an individual or identify an individual in context. This information is not limited to a person's name, address, and contact details, for example a person's IP address, phone IMEI number, gender, and location at a particular time could all be personal information. Organizations are responsible for ensuring the privacy of PI wherever it is stored, including in back-ups, locally stored downloads, and data stored in development environments.

---

**Caution** Personal information (PI) may be at risk of exposure. Depending on local data protection laws organizations may be responsible for mitigating any risk of exposure.

---

## About Reports

---

Reports are collections of meaningful data saved in a common file format, designed according to a particular template, and delivered to the right recipients. As permitted, you can use the set of sample BI Publisher reports or additional reports created by your administrator.

---

### Note

- Project, enterprise, and other types of global data for reports must be automatically or manually published to ensure up-to-date information. See: *Publishing P6 Data (on page 85)*.
- The P6 EPPM sample reports were designed to be run against the small data set included in the sample database. These reports are provided as an example of the product's capability only. Oracle

provides no guarantee, implied or explicit, that the sample reports will run against your database or will produce meaningful data when they are run against your database. You may modify the sample reports to suit your own data set, including adding filter criteria to limit data output or changing filter criteria to suit your data.

---

You can elect to run a report in one of two ways:

- 1) **On-demand:** This type of report generation has many other names, including ASAP, instant, ad-hoc, and "on the fly". As these names imply, the application accepts various input criteria from you in real time and then generates and delivers the selected report to an email address, or prompts you to save or open the file depending on output type.
- 2) **Scheduled:** This type of report generation requires that you first configure the options and other details necessary to generate the report, but doesn't actually generate the report output until the scheduled day and time. You can also generate previously scheduled reports on-demand.

---

### Note

- Your ability to run and schedule reports comes from security settings managed in your P6 reporting software. P6 user access settings determine what, if anything, you will see. For example, to view overhead codes in a Timesheet Report, you need module access for the Reports section of the application as well as resource access for the resources included in the report. Contact your administrator for more information.
  - To see the **Reports** page login as a user with module access to **Enterprise Reports**.
- 

## Reporting in P6 EPPM (Cloud only)

P6 EPPM relies on your P6 reporting software and the P6 EPPM EPPM Extended Schema to produce reports. To run reports in P6 EPPM, you must complete these tasks:

- 1) For publication services, configure publication settings for general data, time distributed data, blob data, and log retention. You can also configure publication services settings for project arbiter, projects, enterprise data, enterprise summaries, resource management, and security.
- 2) Configure and deploy the publication services required to populate the reporting views in the P6 EPPM Extended Schema. See **Working with Publication Services** (on page 83)
- 3) Configure your P6 reporting software to allow P6 to use parameter keys so users do not have to enter field values for reports.
- 4) When you begin working in P6, configure your application settings and global scheduled services. See the *P6 EPPM Application Administration Guide*.
- 5) Provide users with the Edit EPS Costs/Financials project privilege if they need to view project costs in a report generated from the P6 EPPM Extended Schema. See the *P6 EPPM Application Administration Guide*.

---

**Note** A user who has the right to view costs and financials at WBS level

but not at Project level will not see financial data at the WBS level. Although the user has the privilege to view cost and financial data at WBS level, the data is only published at project level.

---

To run P6 reports, you must:

- ▶ Cloud only: In Primavera Administration assign the user access to P6 and either the BI Consumer or BI Author role. The BI Consumer role allows the user to run reports. The BI Author role allows the user to create reports.
- ▶ In your P6 reporting software ensure the user name matches the P6 user name and assign the P6 reports role.
- ▶ In P6 EPPM, assign enterprise reports module access to the user.
- ▶ In P6 EPPM, run publication services to ensure the report processes successfully.

---

**Note** Oracle supports the delivery of reports from P6 EPPM in PDF format via email only.

---

### Assigning Permissions for P6 EPPM Reporting (Cloud only)

Complete the following steps to assign permissions for reporting:

- 1) Log in to Analytics.
- 2) Click **Catalog**.
- 3) Under Shared Folders, highlight the **P6Reports** folder.
- 4) In the Tasks pane, click **Permissions**.
- 5) Select the following checkboxes:
  - ▶ **Apply Permissions to sub-folders**
  - ▶ **Apply permissions to items within this folder**
- 6) Set permissions for the following roles:
  - ▶ **BI Consumer: Open**
  - ▶ **BI Content Author: Traverse**
  - ▶ **BI Service Administrator: Full Control**
- 7) Click **OK**.

## Working with Reports

The reports section of the application hosts an array of reports integrated with your P6 reporting software. The role assigned to you determines the extent of your permissions when using reports in P6.

The screenshot shows the Oracle Primavera P6 EPPM interface. The top navigation bar includes 'Dashboards', 'Portfolios', 'Projects', 'Resources', 'Approvals', 'Reports', and 'Administration'. The 'Reports' tab is selected, showing a list of reports grouped by folder. The 'Schedules' tab is also visible, showing a table of scheduled reports.

Report Name	Default Format	Default Template	Available Formats	Available Templates
Industry Samples				
Utilities				
Online				
T-Week Hit List	html	Clearance Hit List	analyze, html, pdf, rtf, xlsx, pptx	Walkdown Hit List, Clearance Hit List, Material Hit List
Discrepancy Report	html	Discrepancy Report	analyze, html, pdf, rtf, xlsx, pptx	Discrepancy Report
Weekly Resource Loading	html	Resource Loading	analyze, html, pdf, rtf, xlsx, pptx	Resource Loading, Resource Loading (v2)
T-Week Look Ahead	html	Activity Look Ahead_Twk	analyze, html, pdf, rtf, xlsx, pptx	Activity Look Ahead_Twk
High Risk Look Ahead	html	High Risk Look Ahead	analyze, html, pdf, rtf, xlsx, pptx	High Risk Look Ahead
Outage				
Administrative				
Audit				

Schedule Name	Run Type	User	Report Recipients	Status
T-Week Hit List	Daily	weblogic	neelamrutha.peddapati@oracle.com	Pending
T-Week Hit List	Weekly	weblogic	neelamrutha.peddapati@oracle.com	Pending
T-Week Hit List	Monthly	weblogic	neelamrutha.peddapati@oracle.com	Pending

### Reports Screen Elements

Item	Description
1	<p><b>Reports</b> tab: The Reports tab displays the list of reports you have access to run. Run a report on-demand, or use the Schedule detail window to schedule a report run. The remaining screen element descriptions in this table provide more details on the Reports view.</p> <p><b>Schedules</b> tab: The Schedules tab displays the list of all reports you have scheduled to run, organized by run frequency (Once, Daily, Weekly, Monthly). You can suspend or activate the report run by clearing or selecting the Enabled option. Click on a report schedule name and view an explanation of the report in the Description detail window.</p>
2	<p><b>Reports</b> tab work area: Reports are listed by name and grouped by folder. The report list, group names, and hierarchical structure are defined in your P6 reporting software. Your P6 administrator can remove sample reports and create additional reports for your use.</p> <p>From this page, you can view report details including the file formats available for each report. You can also run a report on-demand or print a list of reports in your view.</p>

Item	Description
3	<p><b>Reports</b> tab detail windows:</p> <p><b>Schedules</b> detail window: This detail window lists all the scheduled report runs for the selected report. Use this detail window to add a new scheduled report run, suspend or activate a report run by selecting or clearing the Enabled option, and view the history of report runs. You can also run a scheduled report on-demand from this window.</p> <p><b>Description</b> detail window: This detail window provides an explanation of the report.</p>


## Scheduling Reports

Perform these steps to schedule reports and configure report delivery settings.

To schedule a report:

- 1) Click **Reports**.
- 2) On the **Reports** page:
  - a. Click the **Reports** tab.
  - b. Select a report, and then click the **Schedule** detail window.
- 3) In the **Schedule** detail window, click **Add Schedule...**

---

**Note** You can also schedule a new report using an existing report schedule click  **Row Actions** and then click **Duplicate**.

---

- 4) In the **Add Schedule** dialog box, click the **Options** tab.
- 5) On the **Options** tab:
  - a. In the **Schedule Name** field, enter a name that identifies the report schedule.
  - b. In the **Template** list, choose a template to apply to the report.
  - c. In the **Output Format** list, choose a file format for the delivery of the report.
  - d. Next to the **Delivery Type** field, click ☒ **Send Email** and enter or select email addresses for the intended report recipients.
  - e. In the **Notification** section, choose to send yourself status notification of the report run.
- 6) In the **Add Schedule** dialog box, click the **Parameters** tab.
- 7) On the **Parameters** tab:
  - a. Specify values for the parameters in the **Field Name** column. You can enter values directly in the field or double-click in the field and click **... Select** to open a selection dialog box.

---

### Note

- When selecting project parameters, if you choose to add an EPS to the **Selected Projects** list, only the projects directly under the EPS

are added. If additional EPS elements are under the parent EPS, these projects will not automatically be included in the report; however, you can select additional EPS elements and add them to the **Selected Projects** list.

- To avoid system performance issues, be as specific as possible when entering values for reports. Narrow down your choices to include only what is absolutely necessary.

---

8) In the **Add Schedule** dialog box, click the **Schedule** tab.

9) On the **Schedule** tab:

- a. Select a recurrence pattern from the **Run** list.

---

**Note** If a report is scheduled to run every Monday for 10 weeks and only 2 weeks have passed, the status for the scheduled report run remains *Pending* until all 10 instances of the report have run.

---

- b. Complete the fields shown. The screen elements in this section are dynamically updated based on your selection in the **Run** list.  
For example, for Daily scheduled jobs, enter the **Start Date**, **Finish Date**, **Run Time**, and select one or more days for the report to run.

10) In the **Add Schedule** dialog box, click **Add**.

### Tip

Report parameters to allow flexibility in reporting. For example, Jay in Accounting would like to run a report showing data derived from three active projects. Janice, VP of Strategic Development, wants the same report but is only concerned with one project. They each independently schedule the same report; however, they specify different values for the Project ID report parameter.

## Running Reports On-Demand

Perform these steps to configure report settings and immediately run a report.

To run a report on-demand:

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Select a report.
  - c. Click **Run....**
- 3) In the **Run Report** dialog box:
  - a. In the **Schedule Name** field, enter a name for the report.
  - b. In the **Template** list, choose a template to apply to the report.
  - c. In the **Output Format** list, choose a file format for the delivery of the report.
  - d. In the **Delivery Type** list, choose to have the report sent through email or display the file immediately.
    - If you chose **Email**, click ☒ **Send Email** and enter or select email addresses for the intended report recipients.



- If you chose **File**, the report will display after you click **Run**.
- e. If you chose **Email**, in the **Notification** section, choose to send yourself a status notification of the report run.
- f. In the **Report Parameters** section, specify values for the parameters in the **Field Name** column. You can enter values directly in the field or double-click in the field and click **... Select** to open a selection dialog box.

---

**Note**

- When selecting project parameters, if you choose to add an EPS to the **Selected Projects** list, only the projects directly under the EPS are added. If additional EPS elements are under the parent EPS, these projects will not automatically be included in the report; however, you can select additional EPS elements and add them to the **Selected Projects** list.
  - To avoid system performance issues, be as specific as possible when entering values for reports. Narrow down your choices to include only what is absolutely necessary.
- 

- g. Click **Run**.

**Tip**

When you choose to run a report to be delivered as a file, if the report takes longer than 20 seconds to complete, it will be run as a job service and you will be notified when the report is complete.

## Viewing the Report Run History


Perform these steps to view the list of all runs for the selected report schedule since the last history deletion.

---

**Note** The run history is only captured for scheduled reports, or on-demand reports delivered by Email.

---

To view the report run history:

- 1) Click **Reports**.
- 2) On the **Reports** page:
  - a. Click the **Reports** tab.
  - b. Select a report, and then click the **Schedule** detail window.
- 3) In the **Schedule** detail window, select a schedule name.
- 4) Select  **Row Actions** and click **View History**.
- 5) On the **History** dialog box, review the recent report runs.
  - ▶ To clear the history, click **Clear History**.
  - ▶ Click **Save** or **Cancel** to close the **History** dialog box.

## Sample P6 EPPM Reports

The following sample reports are available with P6. You can use these reports to display various types of project and portfolio data. Your administrator can modify the list of reports available for your use, including removing the sample reports or adding additional reports to your view.

**Note** The P6 EPPM sample reports were designed to be run against the small data set included in the sample database. These reports are provided as an example of the product's capability only. Oracle provides no guarantee, implied or explicit, that the sample reports will run against your database or will produce meaningful data when they are run against your database. You may modify the sample reports to suit your own data set, including adding filter criteria to limit data output or changing filter criteria to suit your data.

### Activity

Report Name	Description	Parameters
<b>Activities That Can Work</b> (on page 19)	Displays activities whose predecessors are all complete and which are ready to start for the project. Also displays all the predecessor activities for each of the activities listed.	Project ID
<b>Activity Look Ahead</b> (on page 20)	Displays activities, along with their dates and status, occurring within specified weeks for the selected projects.	Project ID, Number of Weeks
<b>Activity Relationships</b> (on page 21)	Lists the activities for the selected projects along with their predecessors and successors. Report includes relationship type and lag along with dates and float of the related activities.	Project ID
<b>Calendar</b> (on page 22)	Produces an Excel file showing activities, days, and times in a format similar to a Gantt Chart.	Project ID, Start Date, Number of Days
<b>Cross Project Relationships</b> (on page 23)	Lists the projects and associated activities that are predecessors or successors to the selected project, providing visibility into cross project impacts.	Project ID

<b>Duration Analysis</b> (on page 24)	Compares planned and actual duration of the activities for the selected projects along with upper and lower thresholds to analyze duration estimates.	Project ID
<b>Schedule Report with Notebooks</b> (on page 25)	Provides a list of activities for the selected projects along with all associated notebook topics.	Project ID

### Administrative

Report Name	Description	Parameters
<b>Activity Code Assignments - EPS</b> (on page 35)	Lists the projects with the selected EPS node and shows the EPS Activity Code assignment counts for each project.	EPS ID, EPS Activity Code Specify the EPS Activity Code before selecting the EPS ID.
<b>Activity Code Assignments - Global</b> (on page 36)	Lists projects and shows the Global Activity Code assignment counts for each project.	Global Activity Code
<b>Activity Code Assignments - Project</b> (on page 37)	Lists projects and shows the Project specific Activity Code assignment counts for each project.	Project ID, Project Activity Code Specify the Project Activity Code before selecting the Project ID.
<b>Audit Data - All</b> (on page 26)	Lists the date and time from which and to which audit data is presented and the audit date. Also lists the time the change was made, the application from which the change was initiated, the username which changed the table, and information about the changes made for each change recorded by the auditing feature including the primary key, database column, old and new values, and the operation for each table that was changed.	User, Start Date, End Date Specify the tables to be audited.

<b>Audit Data - Project</b> (on page 27)	Lists the Project Name and Project ID selected for the report the date and time from which and to which audit data is presented and the audit date. Also lists the time the change was made, the application from which the change was initiated, the username which changed the table, and information about the changes made for each change recorded by the auditing feature including the primary key, database column, old and new values, and the operation for each table that was changed.	Start Date, End Date, Project ID Specify the tables to be audited.
<b>Global Calendar Use</b> (on page 38)	Lists all Global, Project, and Resource calendars, including identification of the projects and resources using each calendar.	NA
<b>Profile Privileges</b> (on page 39)	Lists the privileges that are enabled for each global and project-level security profile.	NA
<b>Project Governance Non-Compliance Report</b> (on page 41)	Lists core project-level settings for each project, highlighting setting values that are not compliant.	Project ID
<b>Project Template Management</b> (on page 42)	Lists all project templates along with status, division, and added by person and date.	NA
<b>User Login Report</b> (on page 45)	Lists all users that have logged into P6 EPPM within the specified period.	NA
<b>User Inactivity Report</b> (on page 43)	Lists users that have not logged into P6 EPPM within the specified period.	NA
<b>Users</b> (on page 47)	Lists all users and their personal name along with their associated resource and global security profile.	NA
<b>Users OBS Assignments</b> (on page 49)	Displays all OBS elements along with the corresponding security profile assigned to selected users.	User Name

<b>Users Project Assignments</b> (on page 50)	Displays OBS elements along with the corresponding security profile, EPSs, and Projects assigned to selected users.	User Name
<b>Timesheets</b>	<b>Description</b>	<b>Parameters</b>
<b>Timesheets Status with Notes</b> (on page 32)	Lists timesheets for resources along with the status, submitted and reviewed dates, name of the last reviewer, and associated timesheet notes.	Number of Weeks
<b>Timesheets Status without Notes</b> (on page 33)	Lists timesheets for resources along with the status, submitted and reviewed dates, and name of the last reviewer.	NA
<b>Timesheets with Detailed Hours</b> (on page 30)	Lists timesheets for the specified date range. For each timesheet, the activities and detailed hours per day are provided.	Start Date, End Date

#### Industry Samples - Utilities - Online

<b>Report Name</b>	<b>Description</b>	<b>Parameters</b>
<b>Discrepancy Report</b> (on page 51)	Provides a list of activities which are completed according to the schedule, but where the Work Order is not complete. For each activity, the report lists the ID and Name (as Title), Actual Start, Actual Finish, and the following User Defined Fields: Dpt, Sys, Status, WO, and WO Type.	Project ID
<b>High Risk Look Ahead</b> (on page 52)	Provides a list of high risk activities for a specified number of days from the data date. For each activity, the report lists the ID and Name (as Title), Start, Finish, Remaining Duration, Critical, the following User Defined Fields: Dpt, Sys, Equip ID, WO Type, and WARM.	Project ID, Number of Days

<b><i>T-Week Hit List</i></b> (on page 53)	Provides a list of activities that are on hold, listing the Activity ID, Activity Name (as Title), Start, Finish, Remaining Duration, and the following User Defined Fields: Dpt, Sys, Equip ID, Status, WO, and WO Type.	Project ID, T-Week
<b><i>T-Week Look Ahead</i></b> (on page 54)	Provides a list of activities for the specified T-week, listing the Activity ID, Activity Name (as Title), Start, Finish, Remaining Duration, and the following User Defined Fields: Dpt, Sys, Equip ID, WO, Status, Pri, WO Type, Crit, WARM, and SAP. See or an example.	Project ID, T-Week
<b><i>Weekly Resource Loading</i></b> (on page 55)	Shows the week name, T-Week, Resource name, Scheduled Hours, Available Hours, and Scheduled shown as a percentage of Available.	Project ID, Resource ID

### Industry Samples - Utilities - Outage

Report Name	Description	Parameters
<b><i>Critical Path Report</i></b> (on page 56)	Provides a list of activities in the selected project which are critical for a given number of days. Enter parameters at runtime to define critical (by supplying a maximum Total Float) and a date range (the number of days from the data date). For each critical activity, the report lists the Activity ID, Activity Name (as Title), Start and Finish dates, Original and Remaining Duration, Total Float, and the following User Defined Fields: Dept, System Equip ID, WO, Stat WOT, Pri, Crit, and Risk.	Project ID, Crit Path+, Number of Days

<b>Outage Look Ahead</b> (on page 57)	Shows a list of activities for the specified number of days from the data date. For each activity, the report shows Activity ID, Activity Name (as Title) Start, Finish, Original Duration, Remaining Duration, Total Float, and the following User Defined Fields: Dept, System Equip ID, WO, Stat WOT, Pri, Crit, and Risk.	Project ID, Number of Days
<b>Variance Report</b> (on page 58)	Shows a list of activities which have a schedule variance for the specified number of days from the data date. For each activity, the report provides Activity ID, Activity Name (as Title), Baseline Start, Baseline Finish, Start, Finish, Variance, Total Float, and the following User Defined Fields: Dept, System Equip ID, and Risk.	Project ID, Number of Days

## Portfolio

Report Name	Description	Parameters
<b>Code Assignments</b> (on page 59)	Provides a list of projects for the specified portfolio along with the code values assigned for the selected project code.	Project Code, Portfolio Name
<b>Investment Alignment Chart</b> (on page 60)	Displays a bubble chart that plots selected projects against their strategic and financial rating with the bubble size representing the At Completion Cost.	Project ID
<b>Portfolio Counts</b> (on page 61)	Provides a count of all projects and activities within the selected portfolio. In addition, two pie charts display the number of open and closed issues and risks.	Portfolio Name

<b>Project Portfolio Review</b> (on page 62)	Identifies issues and risks within the selected portfolio and groups them by project. Includes status and priority of the issue or risk along with project-level information.	Portfolio Name
--	---	----------------

## Project

Report Name	Description	Parameters
<b>Baseline Projects Summary</b> (on page 63)	Displays all of a project's baselines including the date the baselines was added, original and current budget, planned labor units, and activity counts.	Project ID
<b>Document Assignments</b> (on page 64)	Provides a list of all documents assigned to activities and WBSs within the specified project, grouped by document category.	Project ID
<b>Issues</b> (on page 65)	Lists all issues identified for the selected projects, grouped by status. The issue details include priority, criticality, and issue description, if provided.	Project ID
<b>Project Earned Value</b> (on page 65)	Displays planned value, actual total cost, earned value, and estimate to complete as periodic and cumulative charts and pivot tables.	Project ID, Start Date, End Date
<b>Project Plan Hierarchy</b> (on page 67)	Displays the project plan which lists all WBSs and activities for the selected project. The activity details include the status, start and finish dates, and the associated activity steps.	Project ID
<b>Project Status Report</b> (on page 68)	Provides a project overview that includes project code values, project costs, issues, risks, status of the milestones, and a list of notebook topics.	Project ID, Project Status



<b>Qualitative Risk Report</b> (on page 69)	Reports on all risks for the select projects. Includes risk information, risk impact assessment, impacted activities, and risk response plans.	Project ID
<b>Risk Scoring</b> (on page 71)	Report of the project risk scoring matrix. Includes threshold definitions grouped by type (Probability, Schedule, Cost, User-defined, and Tolerance) and numeric and alphanumeric probability and impact diagrams (PIDs).	Project ID
<b>S Curve</b> (on page 74)	Displays the originally planned hours, additional work, and work achieved as planned in a bar chart and table.	Project ID, Report Date, Milestone Date
<b>Weekly Schedule Performance</b> (on page 75)	Compares the activity actual finish date to the baseline finish date. Activities are grouped by week and project. The report displays information starting four weeks prior to the date set in the report parameters.	Project ID, 4 Weeks Prior To: <date>

## Resource

Report Name	Description	Parameters
<b>Activity Resource Assignments</b> (on page 76)	Lists resources assigned to each activity in the selected projects. Information includes start and finish dates along with duration.	Project ID
<b>Limit Line</b> (on page 77)	Displays actual units, remaining units, over allocated units, and limit for a Resource.	Resource ID, Start Date, End Date
<b>Resource Code Assignments</b> (on page 78)	Displays a list all resource codes and resource code values along with the resources assigned to each code value.	NA
<b>Resource Role Associations</b> (on page 79)	Displays a list of all roles in the system and the resources assigned to each role. The primary role and proficiency level are identified for each resource.	NA

<b><i>Resource Role Skill Sets</i></b> (on page 80)	Lists all resources along with their assigned roles. The primary role and proficiency level are identified for each role.	NA
<b><i>Resource Stacked Histogram</i></b> (on page 81)	Displays a stacked bar chart showing planned units by month and by project.	Project ID, Resource ID, Start Date, End Date

## Activity Reports

### Activities That Can Work

Figure 1: Activities That Can Work

Baytown, TX - Online Maintenance Work					
<b>Activities with All Predecessors 100% Complete</b>					
Name	Relationship	TF	OD	Start	Status
		Lag	FF	RD	
PM FI-984, 31 RHR PUMP INDIVIDUAL RECIRCULATION (70332400ZZ)			35.2 35.2		Not Started
ADJUST LIMIT SWITCH ON RC-AOV-549-33/O (80161700ZZ)			1 1		Not Started
MANAGEMENT APPROVAL TO EXCEED COLD SHUTDOWN (FO50012)			40 40		Not Started
RETEST FT-926A, SAFETY INJECTION LOOP 3 FLOW (A1030)			8 8		Not Started
SIGNOFF BY MANAGERS FOR COLD SHUTDOWN AP 9.4 (FO49.4CSD)			1 1		Not Started
REPLACE HYDROGEN WITH AIR PER SOP-TG-1 (FO20010)			1 1		Not Started
PM LCV-1127C, HEATER DRAIN TANK BYPASS TO (70566300ZZ)			16 16		Not Started

### Description

Displays a table showing the Name, Relationship Lag, Total and Free Float, Original and Remaining Duration, Start and Finish Dates and Status for every activity which has predecessors or whose predecessors are all complete.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:

- a. Click the **Reports** tab.
- b. Expand the **P6Reports** folder.
- c. Expand the **Activity** folder.
- d. Click **Activities That Can Work**.

---

## Activity Look Ahead

*Figure 2: Activity Look Ahead*

Activity Look Ahead					
Activity Name(ID)	Status	Critical	Percent Complete	Start	Finish
Explore Opportunity(IT1000)	Not Started	Y	0	02/29/2012	03/02/2012
Define Project Charter(IT1010)	Not Started	Y	0	03/05/2012	03/09/2012
Create Plans(IT1020)	Not Started	Y	0	03/09/2012	03/22/2012
Project Start Milestone(IT9001)	Not Started	Y	0	03/02/2012	03/02/2012

### Description

Displays activities, along with dates and status, occurring within specified weeks for the selected projects.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Activity Look Ahead**.

## Activity Relationships

Figure 3: Activity Relationships

Activity Relationships				
Activity Name	Responsibility	Activity Status	Start	Finish
Install Underground Water Lines	FOLEY	Completed	09/27/2015	09/27/2015
Design Building Addition	MILLS	In Progress	09/28/2015	10/05/2015
Start Office Building Addition Project	<b>Pred Name</b>		<b>Responsibility</b>	<b>Finish</b>
	Start Office Building Addition Project		FOLEY	09/27/2015
	<b>Succ. Name</b>		<b>Responsibility</b>	<b>Start</b>
	Review and Approve Designs		MILLS	10/05/2015
Start Office Building Addition Project	FOLEY	Completed	09/27/2015	09/27/2015
Review and Approve Designs	<b>Succ. Name</b>		<b>Responsibility</b>	<b>Start</b>
	Design Building Addition		MILLS	09/28/2015
Review and Approve Designs	MILLS	Not Started	10/05/2015	11/05/2015
Design Building Addition	<b>Pred Name</b>		<b>Responsibility</b>	<b>Finish</b>
	Design Building Addition		MILLS	10/05/2015

### Description

Lists the activities for the selected projects along with their predecessors and successors.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Activity Relationships**.

## Calendar

Figure 4: Calendar

		Production Schedule																									
		(January 1, 2013 - January 30, 2013)																									
Date	Activity ID	12 AM	1 AM	2 AM	3 AM	4 AM	5 AM	6 AM	7 AM	8 AM	9 AM	10 AM	11 AM	12 PM	1 PM	2 PM	3 PM	4 PM	5 PM	6 PM	7 PM	8 PM	9 PM	10 PM	11 PM	PM	
Tue, Jan 1	EC2000																										
	EC2030																										
	EC2070																										
	EC2120																										
	EC2150																										
	EC2170																										
	EC2200																										
	EC2210																										
	EC2080																										
	EC2250																										
	EC2280																										
	EC2290																										
	EC2260																										
	EC2240																										
	EC2310																										
	EC2340																										
	EC2330																										
Wed, Jan 2	EC2000																										
	EC2030																										
	EC2070																										
	EC2120																										
	EC2150																										
	EC2170																										
	EC2200																										
EC2210																											
EC2080																											

## Description

Produces an Excel file which shows activities working on each of the days in the range selected in a format similar to a Gantt Chart.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Calendar**.

## Cross Project Relationships

Figure 5: Cross Project Relationships

Cross Project Relationships	
Project Name / Activity Name (Critical, Relationship Type, Driving, Lag)	
<b>Predecessor Projects impacting Johnstown - Routine Maintenance Work</b>	
Sunset Gorge - Routine Maintenance Work / UNIT AT 100% POWER (No, Start to Start, No, 0)	
Sunset Gorge - Routine Maintenance Work / SIGNOFF BY MANAGERS FOR SYNC TO GRID AP 9.4 (No, Start to Start, No, 0)	
<b>Successor Projects impacted by Johnstown - Routine Maintenance Work</b>	
Baytown, TX - Offline Maintenance Work / RCS AT OPERATING TEMPERATURE (Yes, Start to Start, Yes, 0)	

### Description

Lists the projects and associated activities that are predecessors or successors to the selected project, providing visibility into cross project impacts.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Cross Project Relationships**.

## Duration Analysis

Figure 6: Duration Analysis

Duration Analysis					
Activity	Planned Duration	Actual Duration	High Estimate (25%)	Low Estimate (20%)	Variance %
Set Heat Pump	96	0	120	77	0
Touch-up and Clean-up	19	0	24	15	0
Review and Approve Flooring	224	256	280	179	114
Review Technical Data on Heat Pumps	216	232	270	173	107
Rough-In Plumbing/Piping	19	0	24	15	0
Concrete Foundation Walls	192	0	240	154	0
Form/Pour Concrete Footings	184	0	230	147	0
Assemble Brick Samples	0	0	0	0	0

### Description

Compares planned and actual duration of the activities for the selected projects along with upper and lower thresholds to analyze duration estimates.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Duration Analysis**.



## Schedule Report with Notebooks

Figure 7: Schedule Report with Notebooks

Schedule Report with Notebooks							
Activity	Activity Status	BLI Start	Start	BLI Finish	Finish		
Install Underground Water Lines(A1000)	Completed	08/03/2015	08/03/2015A	08/17/2015	08/18/2015A		
<table><tr><td><b>Notebook Topics:</b> Anticipated Problems</td><td><b>Notebook Description:</b>  Grading and soil conditions will slow this operation. Check estimate. Also, Plumber availability is I</td></tr></table>						<b>Notebook Topics:</b> Anticipated Problems	<b>Notebook Description:</b>  Grading and soil conditions will slow this operation. Check estimate. Also, Plumber availability is I
<b>Notebook Topics:</b> Anticipated Problems	<b>Notebook Description:</b>  Grading and soil conditions will slow this operation. Check estimate. Also, Plumber availability is I						
Design Building Addition(EC1000)	In Progress	08/03/2015	08/03/2015A	10/07/2015	10/05/2015		
Start Office Building Addition Project(EC1010)	Completed	08/03/2015	08/03/2015A	08/03/2015	08/03/2015A		
Review and Approve Designs(EC1030)	Not Started	10/05/2015	10/05/2015	11/05/2015	11/05/2015		

### Description

Provides a list of activities for the selected projects along with all associated notebook topics.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Activity** folder.
  - d. Click **Schedule Report With Notebooks**.


## Administrative Reports

### Audit

#### Audit Data - All

Figure 8: Cross Project Relationships

Audit Data for All Tables

  
PRIMAVERA

From: 2015-05-07T00:00:00.000+05:30 To: 2015-05-28T00:00:00.000+05:30

Audit Date 27-05-2015

Table Name TASK

Time	Application	User	Primary Key(s)	DB Column	Old Value	New Value	Operation
11:46:54	P6WebApp	admin	102887	task_id		102887	I
11:46:54	P6WebApp	admin	102887	proj_id		4408	I
11:46:54	P6WebApp	admin	102887	wbs_id		25306	I
11:46:54	P6WebApp	admin	102887	clndr_id		5829	I
11:46:54	P6WebApp	admin	102887	est_wt		1.00	I
11:46:54	P6WebApp	admin	102887	phys_complete_pct		0.00	I
11:46:54	P6WebApp	admin	102887	rev_fdbk_flag		N	I

### Description

Lists the date and time from which and to which audit data is presented and the audit date. Also lists the time the change was made, the application from which the change was initiated, the username which changed the table, and information about the changes made for each change recorded by the auditing feature including the primary key, database column, old and new values, and the operation (insert, delete, or update) for each table that was changed.

#### Note

- Audit data for fields stored as BLOBs (Binary Large Object) is not captured in this report.
- **Cloud Only:** To collect audit data on BLOB fields, submit a Service Request in My Oracle Support. See: ***How To Retrieve PAUDIT Audit Data From Audit-Enabled Tables With A Blob Field Column Type (KB529380)***  
<https://support.oracle.com/support/?kmExternalId=KB529380>

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:

- Click the **Reports** tab.
- Expand the **P6Reports** folder.
- Expand the **Administrative** folder.
- Expand the **Audit** folder.
- Click **Audit Data - All**.

## Audit Data - Project

Figure 9: Cross Project Relationships

Audit Data for Project

ORACLE  
PRIMAVERA

Project Name: Harbour Pointe Assisted Living CenterProject ID: EC00610

From: 2015-05-19T00:00:00.000+05:30To: 2015-05-30T00:00:00.000+05:30

Audit Date: 27-05-2015

Table Name: TASK

Time	Application	User	Primary Key(s)	DB Column	Old Value	New Value	Operation
11:46:54	P6WebApp	admin	102887	act_equip_qty		0.000000	I
11:46:54	P6WebApp	admin	102887	act_max_drtn		0.000000	I
11:46:54	P6WebApp	admin	102887	act_min_drtn		0.000000	I
11:46:54	P6WebApp	admin	102887	act_prob_drtn		0.000000	I
11:46:54	P6WebApp	admin	102887	act_this_per_equip_qty		0.000000	I
11:46:54	P6WebApp	admin	102887	act_this_per_work_qty		0.000000	I

## Description

Lists the Project Name and Project ID selected for the report the date and time from which and to which audit data is presented and the audit date. Also lists the time the change was made, the application from which the change was initiated, the username which changed the table, and information about the changes made for each change recorded by the auditing feature including the primary key, database column, old and new values, and the operation (insert, delete, or update) for each table that was changed.

**Note**

- Audit data for fields stored as BLOBs (Binary Large Object) is not captured in this report.
- Cloud Only:** To collect audit data on BLOB fields, submit a Service Request in My Oracle Support. See: ***How To Retrieve PAUDIT Audit Data From Audit-Enabled Tables With A Blob Field Column Type (KB529380)***  
<https://support.oracle.com/support/?kmExternalId=KB529380>

**Location**

- Click **Reports**.
- On the **Report** page:
  - Click the **Reports** tab.
  - Expand the **P6Reports** folder.
  - Expand the **Administrative** folder.
  - Expand the **Audit** folder.
  - Click **Audit Data - Project**.

**Approvals****Status Reviews - Pending**

Status Reviewers - Pending												
												Aug 17, 2023
Project	Activity	Type	Status	Submitted User	Resubmitted Date	Last Rejected Date	Held Date	Pending For(Days)	Reviewers Assigned	Review Type	Approved By	Action Required By
EC00610 - Harbour Pointe Assisted Living Center	EC2250 - Fountain/Water Feature	Assignment	Pending	Paul Kim	2023-08-11T06:34:00.000+00:00	2023-08-11T12:04:13.000+00:00		6	Frank Chu, Judy Billings,	EveryoneMustReview		Frank Chu, Judy Billings,
EC00610 - Harbour Pointe Assisted Living Center	EC1610 - Curbs & Paving	Assignment	Pending	Paul Kim				6	Frank Chu, Judy Billings,	EveryoneMustReview		Frank Chu, Judy Billings,
EC00515 - City Center Office Building Expansion	EC1030 - Review and Approve Designs	Assignment	Pending	Paul Kim				6	Frank Chu, Owen McGuire	AnyoneCanReview		Frank Chu, Owen McGuire

**Description**

Lists status updates in a pending state showing which project and activity the status update was submitted against, the assignment level (activity or assignment), and current status of the update. Also lists the user who submitted the update, the date the update was submitted and, if applicable the date of resubmission, the most recent date the update was rejected, the date the update was put on hold, the duration for which the update has been in a pending state, the reviewers assigned to the project, the review type, who the status update was approved by, and the names of the users for whom action is outstanding.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Approvals** folder.
  - e. Click **Status Reviews - Pending**.

## Status Reviews - Not Approved

Status Reviews - Not Approved											
											Aug 17, 2023
Project	Activity	Type	Status	Submitted User	Submission Date	Resubmitted Date	Last Rejected Date	Held Date	Pending For(Days)	Reviewers Assigned	Review Type
EC00610 - Harbour Pointe Assisted Living Center	EC2250 - Fountain/Water Feature	Assignment	Pending	Paul Kim	2023-08-11T00:00:00.000+00:00	2023-08-11T06:34:00.000+00:00	2023-08-11T12:04:13.000+00:00		6	Judy Billings, Alice Wynn, Frank Chu	EveryoneMust Review
EC00610 - Harbour Pointe Assisted Living Center	EC2260 - Entry Feature/Sign Wall	Assignment	Rejected	Paul Kim	2023-08-11T00:00:00.000+00:00		2023-08-11T11:57:39.000+00:00		6	Judy Billings, Alice Wynn, Frank Chu	EveryoneMust Review
EC00610 - Harbour Pointe Assisted Living Center	EC1610 - Curbs & Paving	Assignment	Pending	Paul Kim	2023-08-11T00:00:00.000+00:00				6	Judy Billings, Alice Wynn, Frank Chu	EveryoneMust Review
EC00515 - City Center Office Building Expansion	EC1030 - Review and Approve Designs	Assignment	Pending	Paul Kim	2023-08-11T00:00:00.000+00:00				6	Frank Chu, Owen McGuire	AnyoneCanReview
EC00515 - City Center Office Building Expansion	EC1050 - Assemble Technical Data for Heat Pump	Assignment	Held	Paul Kim	2023-08-11T00:00:00.000+00:00			2023-08-11T11:57:17.000+00:00	6	Owen McGuire, Frank Chu	AnyoneCanReview

## Description

Lists all status updates that have not yet been approved showing which project and activity the status update was submitted against, the assignment level (activity or assignment), and current status of the update. Also lists the user who submitted the update, the date the update was submitted and, if applicable the date of resubmission, the most recent date the update was rejected, the date the update was changed to the held state and the duration for which the update has been in a pending state. For each status update, the reviewers assigned to the project and the type of review required are also provided.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Approvals** folder.

- e. Click **Status Reviews - Not Approved**.

## Timesheets

### Timesheets with Detailed Hours

Figure 10: Timesheets with Detailed Hours

Timesheets with Detailed Hours										
IT Consultant (ITCon) from 4/3/2011 to 4/9/2011										
STATUS: Approved										
Project Name	Activity (ID)	Role ID	Sun 04-03	Mon 04-04	Tue 04-05	Wed 04-06	Thu 04-07	Fri 04-08	Sat 04-09	Total
Project Swordfish	Define Business Requirements * (IT1030)	PM			1 0		1 0			2 0
Project Swordfish	Define System Requirement (IT1040)	PM				3 0	1 0	4 0		8 0
ERP Legacy Merge	Define Project Charter (IT1010)	PM		2 0	2 0			2 0		6 0
ERP Legacy Merge	Create Plans (IT1020)	PM			3 0	1 0				4 0
Digitization Program	Create Plans (IT1020)	PM		2 0	2 0	2 0	4 0			10 0
	General & Accounting (G&A)			4 0						4 0
	Help Desk (Help Desk)					2 0	2 0	2 0		6 0
Total Regular:				8	8	8	8	8		40
Total Overtime:				0	0	0	0	0		0

## Description

Lists timesheets for the specified date range. For each timesheet, the activities and detailed hours per day are provided.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets with Detailed Hours**.

## Timesheets Report - Resource Manager

Timesheets Report - Resource Manager										
Aug 17, 2023										
Resource	Start Date	End Date	Status	Submission Date	Reviewed Date	Last Date Status Changed	Pending For(Days)	Last Reviewed By	Resource Manager	Resource Manager Delegate
KimP - Paul Kim	2023-07-02	2023-07-08	Resubmitted	2023-08-11T06:52:38.000+00:00	2023-08-11T06:52:23.000+00:00	2023-08-12T00:00:35.000+00:00	6	Sam Rickels	Alice Wynn, Sam Rickels, Roy Li	
KimP - Paul Kim	2023-07-09	2023-07-15	Approved	2023-08-11T06:53:05.000+00:00	2023-08-11T06:54:03.000+00:00	2023-08-12T00:00:35.000+00:00	6	Sam Rickels	Alice Wynn, Sam Rickels, Roy Li	
KimP - Paul Kim	2023-08-06	2023-08-12	Approved	2023-08-11T06:49:59.000+00:00	2023-08-11T06:52:24.000+00:00	2023-08-12T00:00:35.000+00:00	6	Sam Rickels	Alice Wynn, Sam Rickels, Roy Li	
KimP - Paul Kim	2023-07-23	2023-07-29	Submitted	2023-08-11T06:53:17.000+00:00		2023-08-12T00:00:35.000+00:00	6		Alice Wynn, Sam Rickels, Roy Li	
KimP - Paul Kim	2023-07-16	2023-07-22	Submitted	2023-08-11T06:53:11.000+00:00		2023-08-12T00:00:35.000+00:00	6		Alice Wynn, Sam Rickels, Roy Li	

### Description

Lists timesheets pending approval by a Resource Manager including the name of the resource assigned, the timesheet period start and end dates, the current status of the timesheet, the submission and reviewed dates, the date the status most recently changed, how long the timesheet has been pending, the user who most recently reviewed the timesheet, the name of the Resource Managers who can approve the timesheet and, any users assigned as a Resource Manager delegate.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets Report - Resource Manager**.

### Timesheet Compliance

### Description

Lists timesheets for resources along with the status, submitted and reviewed dates, name of the last reviewer, and associated timesheet notes.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets Compliance**.

## Timesheets Status with Notes

Figure 11: Timesheets Status with Notes

Timesheets Status with Notes						
04/03/2011 to 04/09/2011						
Resource ID	Resource Name	Submitted Date	Last Reviewer	Reviewed Date	Status	
ITCon	IT Consultant	08/12/2010	rm	08/12/2010	Approved	
<b>Notes History</b>						
12-Aug-2010: IT Consultant On Monday, I had to go to corporate offices to talk to Stan.						
VincentI	Ian Vincent	08/12/2010	rm	08/12/2010	Approved	
<b>Notes History</b>						
12-Aug-2010: Ian Vincent On Thursday I spent 3 hours helping production support with issues on the customer portal page.						
WrenJ	Jo Wren	08/12/2010	rm	08/12/2010	Approved	
ZhuS	Shannon Zhu	08/12/2010	rm	08/12/2010	Approved	

## Description

Lists timesheets for resources along with the status, submitted and reviewed dates, name of the last reviewer, and associated timesheet notes.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets Status with Notes**.



## Timesheets Status without Notes

Figure 12: Timesheets Status without Notes

Timesheets Status without Notes					
08/7/2010 to 08/14/2010					
Resource ID	Resource Name	Submitted Date	Last Reviewer	Reviewed Date	Status
ITCon	IT Consultant	08/12/2010	rm	08/12/2010	Rejected
VincentI	Ian Vincent	08/12/2010	ian		Active
JohnS	John Smith	08/13/2010	rm	08/13/2010	Rejected
JoeP	Joe Programmer	08/12/2010	ian	08/12/2010	Approved
SupportS	Support Staff	08/11/2010	ss	08/13/2010	Rejected
ZhuS	Shannon Zhu	08/12/2010	rm	08/12/2010	Approved
ChenM	Ming Chen	08/12/2010	rm		Active

### Description

Lists timesheets for resources along with the status, submitted and reviewed dates, and name of the last reviewer.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets Status without Notes**.

## Timesheets Report - Project Manager

Timesheets Report - Project Manager											
											Aug 17, 2023
Resource	Start Date	End Date	Status	Projects	Submission Date	Reviewed Date	Last Date Status Changed	Pending For(Days)	Last Reviewed By	Project Manager	Project Manager Delegate
KimP - Paul Kim	2023-07-09	2023-07-15	Approved	EC00501, EC00610	2023-08-11T06:53:05.000+00:00	2023-08-11T06:54:03.000+00:00	2023-08-12T00:00:35.000+00:00	6	Roy Li	Owen McGuire, Judy Billings, Frank Chu, Larry West, Sue Baxter, Alice Wynn, Peg Ithan, Roy Li, Molly Abraham, Dan Sharpe, Ian Vincent, Amit Chopra	
KimP - Paul Kim	2023-07-23	2023-07-29	Submitted	EC00501, EC00610	2023-08-11T06:53:17.000+00:00		2023-08-12T00:00:35.000+00:00	6		Owen McGuire, Judy Billings, Frank Chu, Larry West, Sue Baxter, Alice Wynn, Peg Ithan, Roy Li, Molly Abraham, Dan Sharpe, Ian Vincent, Amit Chopra	
KimP - Paul Kim	2023-07-02	2023-07-08	Resubmitted	EC00501, EC00610	2023-08-11T06:52:38.000+00:00	2023-08-11T06:52:23.000+00:00	2023-08-12T00:00:35.000+00:00	6	Roy Li	Owen McGuire, Judy Billings, Frank Chu, Larry West, Sue Baxter, Alice Wynn, Peg Ithan, Roy Li, Molly Abraham, Dan Sharpe, Ian Vincent, Amit Chopra	
KimP - Paul Kim	2023-08-06	2023-08-12	Approved	EC00501, EC00610	2023-08-11T06:49:59.000+00:00	2023-08-11T06:52:24.000+00:00	2023-08-12T00:00:35.000+00:00	6	Roy Li	Owen McGuire, Judy Billings, Frank Chu, Larry West, Sue Baxter, Alice Wynn, Peg Ithan, Roy Li, Molly Abraham, Dan Sharpe, Ian Vincent, Amit Chopra	
KimP - Paul Kim	2023-07-16	2023-07-22	Submitted	EC00501, EC00610	2023-08-11T06:53:11.000+00:00		2023-08-12T00:00:35.000+00:00	6		Owen McGuire, Judy Billings, Frank Chu, Larry West, Sue Baxter, Alice Wynn, Peg Ithan, Roy Li, Molly Abraham, Dan Sharpe, Ian Vincent, Amit Chopra	

## Description

Lists timesheets pending approval by any Project Manager including the name of the resource assigned, the timesheet period start and end dates, the current status of the timesheet, the project against which the timesheet was submitted, the submission and reviewed dates, the date the status most recently changed, how long the timesheet has been pending, the user who most recently reviewed the timesheet, the names of the Project Managers who can approve the timesheet and, any users assigned as a Project Manager delegate.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Expand the **Timesheets** folder.
  - e. Click **Timesheets Report - Project Manager**.

## Activity Code Assignments - EPS

Figure 13: Activity Code Assignments - EPS

EPS Activity Code Assignments			
EPS ID: Energy			
EPS Name: Energy Services			
Activity Code			Count
CREW			1
Project Name: Red River - Refuel Outage		Project ID: NRG00950	
<u>Code Value</u>	<u>Code Description</u>		<u>Count</u>
CREW	Crew Description		1
Activity Code			Count
Foreman			97
Project Name: Springfield - Refuel Outage		Project ID: NRG01000-1	
<u>Code Value</u>	<u>Code Description</u>		<u>Count</u>
BA	Bill Anderson		22
HD	Henry Davis		32
MW	Mark White		28
SW	Steve Williams		15
Activity Code			Count
Project Manager			76
Project Name: Springfield - Refuel Outage		Project ID: NRG01000-1	
<u>Code Value</u>	<u>Code Description</u>		<u>Count</u>
DJ	Dave Jones		27
JS	Joe Smith		14
MJ	Mike Johnson		35

### Description

Provides a list of EPS level Activity Codes showing the number of assignments for each value of each code broken down by project.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Activity Code Assignments - EPS**.

## Activity Code Assignments - Global

Figure 14: Global Activity Code Assignments

Global Activity Code Assignments			
Activity Code			Count
Work Order Type			269
Project Name: Baytown, TX - Online Maintenance Work		Project ID: NRG00870-1	
<u>Code Value</u>	<u>Code Description</u>		<u>Count</u>
CM	Corrective Maintenance		19
DM	Deficient Maintenance		38
OM	Other Maintenance		42
PM	Preventative Maintenance		39
Project Name: Springfield - Refuel Outage		Project ID: NRG01000-1	
<u>Code Value</u>	<u>Code Description</u>		<u>Count</u>
CM	Corrective Maintenance		18
DM	Deficient Maintenance		35
OM	Other Maintenance		41
PM	Preventative Maintenance		37

### Description

Provides a list of Global Activity Codes showing the number of assignments for each value of each code broken down by project.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Activity Code Assignments - Global**.

## Activity Code Assignments - Project

Figure 15: Project Activity Code Assignments

Project Activity Code Assignments		
Project ID: NRG00920		
Project Name: Buckingham - Nuclear Outage Work		
Activity Code		Count
Crew		139
<u>Code Value</u>	<u>Code Description</u>	<u>Count</u>
AM001	MGM Review	4
EM001	Elect Maint - Global Crew	3
HP001	Health Physics - Global Crew	1
IC001	Departmental - Global Crew	17
ICJB1	Contractors Days	1
ICJB5	IC Days - Global	2
MM001	(MECH/ELEC) - Global Crew	5
MMBP1	Bill Petrosi	2
MMFL1	Fausto Lord	1
MMJA1	Jack Arcate	1
OP001	Operations - Global Crew	96
OPTG1	Operations Test Group	6

### Description

Provides a list of Project Activity Codes showing the number of assignments for each value of each code.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Activity Code Assignments - Project**.

## Global Calendar Use

Figure 16: Calendar Use

Global Calendar Use			
Calendar Name			
7x24			
Project ID	Project Name	Resource ID	Resource Name
NRG00870	Baytown, TX - Online Maintenance Work	INSP	Inspections
		Hydro	Hydroblaster
		Material	Material Resources
6x24			
Corporate - Standard Full Time (Default Calendar)			
		Resource ID	Resource Name
		SinghD	Deepak Singh
		SharpeD	Dan Sharpe

## Description

Lists all global calendars, including identification of the projects and resources using each calendar.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Global Calendar Use**.

## Never Logged Users

Figure 17: Users

Never Logged Users	
USER ID	USER NAME
102	HillF
106	IthanP
107	JacksonL

### Description

Lists users who have never logged into P6.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Never Logged Users**.

## Profile Privileges

Figure 18: Profile Privileges

Profile Privileges	
Profile Scope	
Security Profile	
Security Privilege	
<hr/>	
GLOBAL	
<No Global Privileges>	
Administrator	
Add Global Activity Codes	
Add Global Issue Codes	
Add Project Codes	
Add Resource Codes	
Add Resources	
Add/Delete Secure Codes	
Add/Edit/Delete Activity Step Templates	
Add/Edit/Delete Categories and Overhead Codes	

### Description

Lists the privileges that are enabled for each global and project-level security profile.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Profile Privileges**.

---

### Project Calendar Use

Project Calendar Use		
Project Id	Project Name	Calendars Used
NRG00870	Baytown, TX - Online Maintenance Work	12S,19-7  24  2S,7-19

### Description

Lists the calendars used by the selected projects grouped by project.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Project Calendar Use**.



## Project Governance Non-Compliance Report

Figure 19: Project Governance Non-compliance Report

Project Governance Non-Compliance Report						
	Activity Default Duration Type	When updating units or costs	Link Actual to date and actual this period	Allow Negative Actual Units	Resource can edit assignment % complete	Primary Resource can mark Activity Complete
Desired Project Settings	Fixed Duration & Units/Time	No	Yes	Yes	No	Yes
Rural Office Building Addition	Fixed Duration & Units	No	Yes	No	No	Yes
Saratoga Senior Community - B3	Fixed Duration & Units/Time	No	Yes	No	Yes	Yes

### Description

Lists core project-level settings for each project, highlighting setting values that are not compliant.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Project Governance Non-Compliance Report**.

## Project Template Management

Figure 20: Project Template Management

Project Template Management					
Template Name	Status	Type	Division	Added By	Date Added
Order Fulfillment Phase II	Active		Plastics	admin	1/25/2010
GIS Interface Project	Active		Wireless	admin	1/25/2010
Online Invoice Generation Project	Active		Specialty Chemicals	admin	1/25/2010
Alliance Portal Integration Project	What-If		Energy Services	admin	1/25/2010
Lead Qualification Project	Active		Media & Entertainment	admin	1/25/2010
Order Management Redesign	Active		Network Operations	admin	1/25/2010
Nexus Project	What-If		Specialty Chemicals	admin	1/25/2010

### Description

Lists all project templates along with status, division, and added by person and date.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Project Template Management**.

## User Inactivity Report

Figure 21: Activity Code Assignments - EPS

User Inactivity Report			
USER_ID	USER_NAME	LAST_LOGIN (SERVER TIME)	CREATED_DATE
153	MarshallG		01-07-2024
142	RileyP		20-06-2024
152	ShawH		01-07-2024
172	LincolnR		31-07-2024
122	JacksonL		24-05-2024
93	HillF		13-05-2024
162	BaxterS		30-07-2024
92	WynnA		13-05-2024
102	lthanP		14-05-2024
132	WestL		18-06-2024
182	RickelsS		02-08-2024
113	LeeC		16-05-2024
303	CaseyA		30-08-2024

### Description

Provides a list of users that have not logged into P6 EPPM in the time period specified in the Time interval to store user login information setting in Application Settings. Shows the user ID, user name, most recent log out date and time, and the creation date of the user account.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **User Not Logged In Report**.

**User Inactivity Report - Active Users Only**

User Inactivity Report - Active Users Only		
USER_ID	USER_NAME	LAST_LOGIN (SERVER TIME)
59	YoungJ	
63	JohnsonR	
69	MarshallG	
67	PrescottW	
54	ResnerW	

**Description**

Provides a list of active users that have not logged into P6 EPPM in the time period specified in the Time interval to store user login information setting in Application Settings. Shows the user ID, user name, and most recent log out date and time.

**Location**

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **User Inactivity Report - Active Users Only**.

## User Login Report

Figure 22: Activity Code Assignments - EPS

User Login Report						
USER_ID	USER_NAME	LOG_IN_DATE_AND_TIME (SERVER_TIME)	LOG_OUT_DATE_AND_TIME (SERVER_TIME)	TOTAL_TIME LOGGED_IN(M)	APP_NAME	HOST_NAME
92	LaffertyV	23-04-2018 05:42:42	23-04-2018 05:44:01	1.32	P6 Web	P6Server
92	LaffertyV	23-04-2018 05:42:42	23-04-2018 05:44:01	1.32	P6 Web	P6Server
96	LiR	23-04-2018 05:35:52	23-04-2018 05:47:08	11.27	P6 Web	P6Server
96	LiR	23-04-2018 05:35:50	23-04-2018 05:47:08	11.3	P6 Web	P6Server
96	LiR	23-04-2018 05:35:50	23-04-2018 05:47:08	11.3	P6 Web	P6Server
96	LiR	23-04-2018 05:25:27	23-04-2018 05:35:41	10.23	P6 Web	P6Server
96	LiR	23-04-2018 05:25:25	23-04-2018 05:35:41	10.27	P6 Web	P6Server
96	LiR	23-04-2018 05:25:25	23-04-2018 05:35:41	10.27	P6 Web	P6Server
103	LaffertyV	23-04-2018 05:23:59	23-04-2018 05:27:23	3.4	P6 Web	P6Server
103	SinghD	23-04-2018 05:23:59	23-04-2018 05:27:23	3.4	P6 Web	P6Server
91	ResnerW	23-04-2018 04:31:37	23-04-2018 05:37:35	65.97	P6 Web	P6Server
91	ResnerW	23-04-2018 04:31:37	23-04-2018 05:37:35	65.97	P6 Web	P6Server
103	SinghD	23-04-2018 04:23:44	23-04-2018 04:38:17	14.55	P6 Web	P6Server
103	SinghD	23-04-2018 04:23:44	23-04-2018 04:38:17	14.55	P6 Web	P6Server
91	ResnerW	23-04-2018 04:11:34	23-04-2018 05:22:35	71.02	P6 Web	P6Server
91	ResnerW	23-04-2018 04:11:34	23-04-2018 05:22:35	71.02	P6 Web	P6Server
103	SinghD	23-04-2018 04:11:25	23-04-2018 05:16:35	65.17	P6 Web	P6Server

### Description

Provides a list of users logged into P6 EPPM within the period specified in the Time interval to store user login information setting in Application Settings. Shows the user ID, user name, login date and time, logout date and time, the total time the user was logged in, the application the user logged into, and the server for that application.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **User Login Report**.

### User Login Report - Active Users Only

User Login Report- Active Users Only					
USER_ID	USER_NAME	LOG_IN_DATE_AND_TIME (SERVER_TIME)	LOG_OUT_DATE_AND_TIME(SERVER_TIME)	TOTAL_TIME LOGGED_IN(HH:MM:SS)	APP_NAME
108	RickelsS	06-05-2022 15:06:30	06-05-2022 15:13:13	0:6:43	P6 Web
105	WynnA	06-05-2022 15:04:29	06-05-2022 15:09:45	0:5:16	P6 Web
105	WynnA	06-05-2022 14:59:02	06-05-2022 16:01:28	1:2:26	P6 Web
109	LiR	06-05-2022 15:05:01	06-05-2022 17:08:28	2:3:27	P6 Web
109	LiR	06-05-2022 15:05:01	06-05-2022 17:06:29	2:1:28	P6 Web
110	AbrahamM	06-05-2022 15:12:09	06-05-2022 17:08:28	1:56:19	P6 Web
104	BaxterS	06-05-2022 15:09:44	06-05-2022 17:08:28	1:58:44	P6 Web
103	WestL	06-05-2022 15:13:12	06-05-2022 15:14:52	0:1:40	P6 Web
111	WrenJ	06-05-2022 15:08:39	06-05-2022 15:13:57	0:5:18	P6 Web

#### Description

Provides a list of active users logged into P6 EPPM within the period specified in the Time interval to store user login information setting in Application Settings. Shows the user ID, user name, login date and time, logout date and time, the total time the user was logged in, and the application the user logged into.

#### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **User Login Report - Active Users Only**.

## Users

Users			
Login Name	Personal Name	Resource	Global Profile
AbrahamM	Molly Abraham	AbrahamM	Administrator
BaxterS	Sue Baxter	BaxterS	Resource Manager
BillingsJ	Judy Billings	BillingsJ	Executive / Stakeholder
ChopraA	Amit Chopra	ChopraA	Resource Manager
ChuF	Frank Chu	Chuf	Status Updater
HillF	Frank Hill	HillF	Status Updater
IthanP	Peg Ithan	IthanP	PMO
JacksonL	Lendell Jackson	JacksonL	Status Updater
LeeC	Cindy Lee	LeeC	Administrator
LiR	Roy Li	LiR	Project Manager
LincolnR	Robert Lincoln	LincolnR	PMO
RickelsS	Sam Rickels	RickelsS	Project Manager
WestL	Larry West	WestL	Project Manager
WrenJ	Jo Wren	WrenJ	Project Manager
WynnA	Alice Wynn	WynnA	PMO

## Description

Lists all users and their personal name along with their associated resource and global security profile.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Users**.

**Users - Active Users Only**

<b>Users</b>			
<b>Login Name</b>	<b>Personal Name</b>	<b>Resource</b>	<b>Global Profile</b>
AbrahamM	Molly Abraham	AbrahamM	Administrator
BaxterS	Sue Baxter	BaxterS	Resource Manager
HillF	Frank Hill	HillF	Status Updater
IthanP	Peg Ithan	IthanP	PMO
JacksonL	Lendell Jackson	JacksonL	Status Updater
LiR	Roy Li	LiR	Project Manager
RickelsS	Sam Rickels	RickelsS	Project Manager
WestL	Larry West	WestL	Project Manager
WrenJ	Jo Wren	WrenJ	Project Manager
WynnA	Alice Wynn	WynnA	PMO

**Description**

Lists all active users including their personal name, the associated resource, and their global security profile.

**Location**

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Users - Active Users Only**.



## Users OBS Assignments

Figure 23: User OBS Assignment

Users OBS Assignment		
Name (count)		
User Name	OBS Name	Security Profile
<b>biz Business User (1)</b>		
	Enterprise	<Project Superuser>
<b>exec Executive (1)</b>		
	Enterprise	<Project Superuser>
<b>pm Project Manager (1)</b>		
	Enterprise	<Project Superuser>
<b>pmo PMO (1)</b>		
	Enterprise	<Project Superuser>
<b>rm Resource Manager (1)</b>		
	Enterprise	<Project Superuser>

### Description

Displays all OBS elements along with the corresponding security profile assigned to selected users.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Users OBS Assignments**.

## Users Project Assignments

Figure 24: User Project Assignments

Users Project Assignments	
Name (count)	
<b>biz Business User (1)</b>	
OBS Name	Security Profile
Enterprise	<Project Superuser>
EPS	
All Initiatives(Enterprise),Project Templates(Templates), Project	
<b>exec Executive (1)</b>	
OBS Name	Security Profile
Enterprise	<Project Superuser>
EPS	
All Initiatives(Enterprise),Project Templates(Templates), Project	

### Description

Displays OBS elements along with the corresponding security profile, EPSs, and Projects assigned to selected users.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Administrative** folder.
  - d. Click **Users Project Assignments**.

## Industry Samples

### Utilities

#### Online

#### Discrepancy Report

Figure 25: Discrepancy Report

Discrepancy Report									
Data Date: 06/02/13 00:00									
Springfield - Online Maintenance Work									
ACT ID	Dpt	Sys	Equip ID	Title	Actual Start	Actual Finish	Status	WO	WO Type
99001200-01	MM	907	1CD01B	1B EDG Starting Air Compressor: Quarterly PM	04/16/13 07:00	04/16/13 11:00	W	99001200	PM
99001201-01	MM	907	1CD01A	1A EDG Starting Air Compressor: Quarterly PM	04/16/13 07:00	04/16/13 11:00	W	99001201	PM
99001202-01	MM	907	1CD01A	1A EDG Starting Air Compressor: Monthly PM	04/16/13 07:00	04/16/13 11:00	W	99001202	PM
99001203-01	MM	907	1CD01B	1B EDG Starting Air Compressor: Monthly PM	04/16/13 07:00	04/16/13 11:00	W	99001200	PM
99001207-01	ELE	901	1P01C	1C Intake Cooling Water Pump: Filter Replacement	05/23/13 13:00	05/23/13 15:00	W	99001207	PM
99001205-01	MM	901	1P01A	1A Intake Cooling Water Pump:Oil Sample	05/29/13 08:00	05/29/13 10:00	W	99001205	PM
99001206-01	MM	901	1P01B	1B Intake Cooling Water Pump:Oil Sample	05/29/13 08:00	05/29/13 10:00	W	99001206	PM

### Description

Provides a list of activities which are completed according to the schedule, but where the Work Order is not complete. For each activity, the report lists the ID and Name (as Title), Actual Start, Actual Finish, and the following User Defined Fields: Dpt, Sys, Status, WO, and WO Type.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Online** folder.
  - f. Click **Discrepancy Report**.

## High Risk Look Ahead

Figure 26: High Risk Look Ahead

High Risk Look Ahead

Number of Days: 30

Data Date: 06/02/13 00:00

Springfield - Online Maintenance Work

ACT ID	Dpt	Sys	Equip ID	Title	Start Dt	Finish Dt	RD	Pri	WO Type	Crit	WARM
99001234-01	ELE	901	1P01A	1A Intake Cooling Water Pump: Motor Inspection	06/03/13 10:00	06/03/13 19:00	8	D	PM		HIGH
99001235-01	ELE	901	1P01B	1B Intake Cooling Water Pump: Motor Inspection	06/17/13 10:00	06/17/13 19:00	8	D	PM		HIGH
99001236-01	ELE	901	1P01C	1C Intake Cooling Water Pump: Motor Inspection	06/19/13 10:00	06/19/13 19:00	8	D	PM		HIGH
99001247-01	ELE	903	MOV-1-1001	AFW Steam Supply MOV From A S/G: Grease Inspection	06/25/13 07:00	06/25/13 14:00	6	D	PM		HIGH
99001248-01	ELE	903	MOV-1-1001	AFW Steam Supply MOV From A S/G: Static Test	06/25/13 16:00	06/26/13 00:00	8	D	PM		HIGH

### Description

Provides a list of high risk activities for a specified number of days from the data date. For each activity, the report lists the ID and Name (as Title), Start, Finish, Remaining Duration, Critical, the following User Defined Fields: Dpt, Sys, Equip ID, WO Type, and WARM.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Online** folder.
  - f. Click **High Risk Look Ahead**.

## T-Week Hit List

Figure 27: T-Week Hit List

Clearance Not Ready

T-0 to T-12

Data Date: 06/02/13 15:00

Springfield - Online Maintenance Work

ACT ID	Dpt	Sys	Equip ID	Title	Start Dt	Finish Dt	RD	Status	WO	WO Type
99001234-01	ELE	901	1P01A	1A Intake Cooling Water Pump: Motor Inspection	06/03/13 10:00	06/03/13 19:00	8	R	99001234	PM
99001254-01	MM	907	1CD01B	1B EDG Starting Air Compressor: Quarterly PM	06/05/13 07:00	06/05/13 11:00	4	R	99001254	PM
99001268-01	MM	904	P03A	A Service Water Pump: Annual PM	06/05/13 07:00	06/05/13 11:00	4	P	99001268	PM
99012452-01	MM	904	P03A	A Service Water Pump: Discharge Isolation Valve Leaking	06/05/13 07:00	06/05/13 14:00	6	P	99001252	DM
99012451-01	MM	904	P03A	A Service Water Pump: IB/OB Oil Change	06/05/13 07:00	06/05/13 16:00	8	R	99001251	DM
99001247-01	ELE	903	MOV-1-1001	AFW Steam Supply MOV From A S/G: Grease Inspection	06/25/13 07:00	06/25/13 14:00	6		99001247	PM
99001263-01	IC	913	PT-1-100A	Replace Pressure Transmitter	06/26/13 07:00	06/26/13 16:00	8	R	99001262	PM
99001249-01	ELE	903	MOV-1-1002	AFW Steam Supply MOV From B S/G: Grease Inspection	07/09/13 07:00	07/09/13 14:00	6		99001249	PM

## Description

Provides a list of activities that are on hold, listing the Activity ID, Activity Name (as Title), Start, Finish, Remaining Duration, and the following User Defined Fields: Dpt, Sys, Equip ID, Status, WO, and WO Type.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Online** folder.
  - f. Click **T-Week Hit List**.

## T-Week Look Ahead

Figure 28: T-Week Look Ahead

T-Week Look Ahead T-1

08/11/2013 to 08/17/2013

Data Date: 08/10/13 00:00

Baytown, TX - Online Maintenance Work

ACT ID	Dpt	Sys	Equip ID	Title	Start Dt	Finish Dt	RD	WO	Status	Pri	WO Type	Crit	WARM	SAP
FO30010				COOLDOWN RCS TO LESS THAN 350 DEGREES (MODE 4)	08/07/13 09:00	08/16/13 16:00	39		-		PM	L		
A1080				31 RHR PUMP INDIVIDUAL RECIRCULATION	08/10/13 01:00	08/11/13 03:00	24				PM	N		
80161700ZZ				ADJUST LIMIT SWITCH ON RC-AOV-549-33/O	08/12/13 08:00	08/12/13 09:00	1		R		PM	L		
FO10011				BREAKER OPEN, START THE OUTAGE	08/12/13 08:00	08/12/13 09:00	1		-		PM	N		
FO20007				PLACE TURBINE GENERATOR ON TURNING GEAR PER	08/12/13 08:00	08/12/13 09:00	1		-		PM	L		
FO20010				REPLACE HYDROGEN WITH AIR PER SOP-TG-1	08/12/13 08:00	08/12/13 09:00	1		-		DM	L		
FO49.4CSD				SIGNOFF BY MANAGERS FOR COLD SHUTDOWN AP 9.4	08/12/13 08:00	08/12/13 09:00	1		-		OM	N		
OPS980017H				HANG SAFETY TAG (PTO) FOR BIT HEADER	08/12/13 08:00	08/12/13 09:00	1		-		OM	N		
A1240				RAISE RX POWER FROM 25% TO 30%	08/12/13 08:00	08/12/13 10:00	2				PM	N		
70172804ZZ				PM 52/RCP33, TRIP CHECKS FOR BREAKERS	08/12/13 08:00	08/12/13 10:00	2		R		PM	L		
FO10009				SECURE SECOND CONDENSATE PUMP	08/12/13 08:00	08/12/13 11:00	3		-		CM	L		
A1170				REPAIR BROKEN SEAL TIGHT ON FT-928A	08/12/13 08:00	08/12/13 12:00	4				DM	C		
FO10008				TRIP GENERATOR, OFF THE GRID	08/12/13 08:00	08/12/13 14:00	5		-		OM	N		
80047201ZZ				RETEST FT-928A, SAFETY INJECTION LOOP 3 FLOW	08/12/13 08:00	08/12/13 17:00	8		I		PM	C		
FO10010				REDUCE REACTOR POWER TO LESS THAN 4% - (MODE 2)	08/12/13 08:00	08/12/13 17:00	8		-		OM	N		

## Description

Provides a list of activities for the specified T-week, listing the Activity ID, Activity Name (as Title), Start, Finish, Remaining Duration, and the following User Defined Fields: Dpt, Sys, Equip ID, WO, Status, Pri, WO Type, Crit, WARM, and SAP.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Online** folder.
  - f. Click **T-Week Look Ahead**.

## Weekly Resource Loading

Figure 29: Weekly Resource Loading

Resource Loading by Week

T-0 to T-18

Data Date: 06/02/13 00:00

Week		Resource	Scheduled	Available	%	Thresholds
06/02/2013	T-0	Electrical Maintenance	28	24	117	>105
06/09/2013	T-1	Electrical Maintenance	48	24	200	>88
06/16/2013	T-2	Electrical Maintenance	56	48	117	>80
06/23/2013	T-3	Electrical Maintenance	32	16	200	>70
06/30/2013	T-4	Electrical Maintenance	28	24	117	<70
07/07/2013	T-5	Electrical Maintenance	32	16	200	
07/14/2013	T-6	Electrical Maintenance	56	224	25	

### Description

Shows the week name, T-Week, Resource name, Scheduled Hours, Available Hours, and Scheduled shown as a percentage of Available.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Online** folder.
  - f. Click **Weekly Resource Loading**.

## Outage

### Critical Path Report

Figure 30: Critical Path Report

Critical Path Report

Total Float <= 2

Number of Days: 5

Data Date:04/18/13 00:00

Springfield - Refuel Outage

Act ID	Dept	System Equip ID	Title	Start Dt Finish Dt	OD RD	TF	WO	Stat WOT	Pri Crit	Risk
70172304ZZ	IC	000	PM 52/RCP31, TRIP CHECKS FOR BREAKERS	04/18/13 08:00	2	0	90014321	W	N	
				04/18/13 10:00	2			OM		
70172404ZZ	IC	000	PM 52/RCP32, TRIP CHECKS FOR BREAKERS	04/18/13 10:00	38	0		W	L	
				04/24/13 17:00	38			PM		

### Description

Provides a list of activities in the selected project which are critical for a given number of days. Enter parameters at runtime to define critical (by supplying a maximum Total Float) and a date range (the number of days from the data date). For each critical activity, the report lists the Activity ID, Activity Name (as Title), Start and Finish dates, Original and Remaining Duration, Total Float, and the following User Defined Fields: Dept, System Equip ID, WO, Stat WOT, Pri, Crit, and Risk.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Outage** folder.
  - f. Click **Critical Path Report**.



## Outage Look Ahead

Figure 31: Outage Look Ahead

### Outage Look Ahead

Number of Days: 30

Data Date: 08/10/13 00:00

#### Baytown, TX - Online Maintenance Work

Act ID	Dept	System Equip ID	Title	Start Dt Finish Dt	OD RD	TF	WO	Stat WOT	Pri Crit	Risk
FO30010			COOLDOWN RCS TO LESS THAN 350 DEGREES (MODE 4)	08/07/13 09:00 08/16/13 16:00	39 39			- PM	 L	
A1090			SWAP FEEDWATER FROM MANUAL TO AUTOMATIC	08/10/13 01:00 08/10/13 05:00	4 4			 OM	 N	
A1120			TRANSFER RCS TEMP CONTROL TO STEAM DUMPS	08/10/13 01:00 08/10/13 05:00	4 4			 DM	 C	
A1080			31 RHR PUMP INDIVIDUAL RECIRCULATION	08/10/13 01:00 08/11/13 03:00	24 24			 PM	 N	
80161700ZZ			ADJUST LIMIT SWITCH ON RC-AOV-549-33/O	08/12/13 08:00 08/12/13 09:00	1 1			R PM	 L	
FO10011			BREAKER OPEN, START THE OUTAGE	08/12/13 08:00 08/12/13 09:00	1 1			- PM	 N	

### Description

Shows a list of activities for the specified number of days from the data date. For each activity, the report shows Activity ID, Activity Name (as Title) Start, Finish, Original Duration, Remaining Duration, Total Float, and the following User Defined Fields: Dept, System Equip ID, WO, Stat WOT, Pri, Crit, and Risk.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Outage** folder.
  - f. Click **Outage Look Ahead**.

## Variance Report

Figure 32: Variance Report

Variance Report

Project Baseline:NRG01000-1 - B1

Date Added:06/24/13 15:07

Number of Days: 20

Data Date: 04/18/13 00:00

Springfield - Refuel Outage

Act ID	Dept	System Equip ID	Title	BL Start Dt BL Finish Dt	Start Dt Finish Dt	Var	TF	Risk
60788900ZZ	MM	000	REPAIR INTERNAL LEAK FOR VALVE 5EX-FCV-1206	04/25/13 08:00	04/26/13 08:00	-8	168	R
				04/29/13 17:00	04/30/13 17:00	-8		
A1040	OPS	000 LCV-1124	POST WORK TEST AFTER LCV-1124 (AO) CALIBRATION	05/01/13 17:00	05/02/13 01:00	-7	579	R
				05/02/13 02:00	05/02/13 09:00	-7		
70175204ZZ	IC	000	PM 52/HDP31, TRIP CHECKS FOR BREAKERS	05/02/13 08:00	05/03/13 08:00	-8	151	R
				05/02/13 09:00	05/03/13 09:00	-8		
FO30003	OPS	000	ADJUST BORON CONCENTRATION TO HSD XENON FREE	05/02/13 08:00	05/03/13 08:00	-8	148	R
				05/02/13 12:00	05/03/13 12:00	-8		
70174804ZZ	IC	000	PM 52/CP31, TRIP CHECKS FOR BREAKERS	05/02/13 08:00	05/03/13 08:00	-8	146	R
				05/02/13 15:00	05/03/13 15:00	-8		
FO40005	OPS	000	DEPRESSURIZE RCS TO 350 PSIG	05/02/13 08:00	05/03/13 08:00	-8	140	R
				05/03/13 12:00	05/06/13 12:00	-8		

### Description

Shows a list of activities which have a schedule variance for the specified number of days from the data date. For each activity, the report provides Activity ID, Activity Name (as Title), Baseline Start, Baseline Finish, Start, Finish, Variance, Total Float, and the following User Defined Fields: Dept, System Equip ID, and Risk.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Industry Samples** folder.
  - d. Expand the **Utilities** folder.
  - e. Expand the **Outage** folder.
  - f. Click **Variance Report**.

## Portfolio Reports

### Code Assignments

Figure 33: Code Assignments

Code Assignments			
<b>City Center Office Building Addition</b>			
<u>Business Segment</u>	<u>Current Phase</u>	<u>Project Manager</u>	<u>Strategic Objective</u>
1004050	Design	Thomas	Rev Growth
Commercial Construction	Design	Bob Thomas	Revenue Growth
<b>Baytown, TX - Offline Maintenance Work</b>			
<u>Business Segment</u>	<u>Current Phase</u>	<u>Project Manager</u>	<u>Strategic Objective</u>
1023980	Initiation	Thomas	Reduced Cycle
Energy Services	Initiation	Bob Thomas	Reduced Cycle Time

### Description


Provides a list of projects for the specified portfolio along with the code values assigned for the selected project code.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Portfolio** folder.
  - d. Click **Code Assignments**.

## Investment Alignment Chart

Figure 34: Investment Alignment Chart

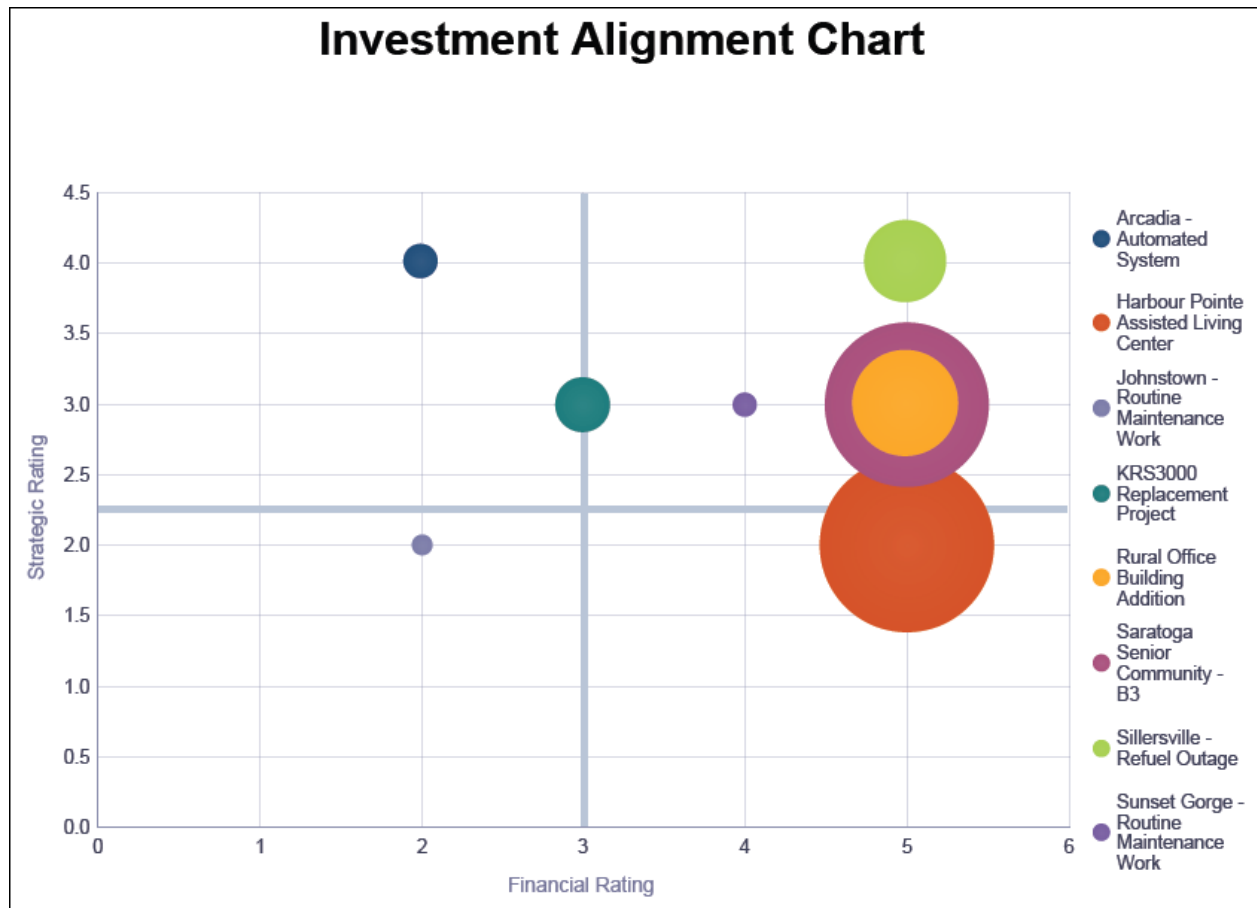

### Description


Displays a bubble chart that plots selected projects against their Strategic and Financial Rating with the bubble size representing the At Completion Cost.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Portfolio** folder.
  - d. Click **Investment Alignment Chart**.

## Portfolio Counts

Figure 35: Portfolio Counts

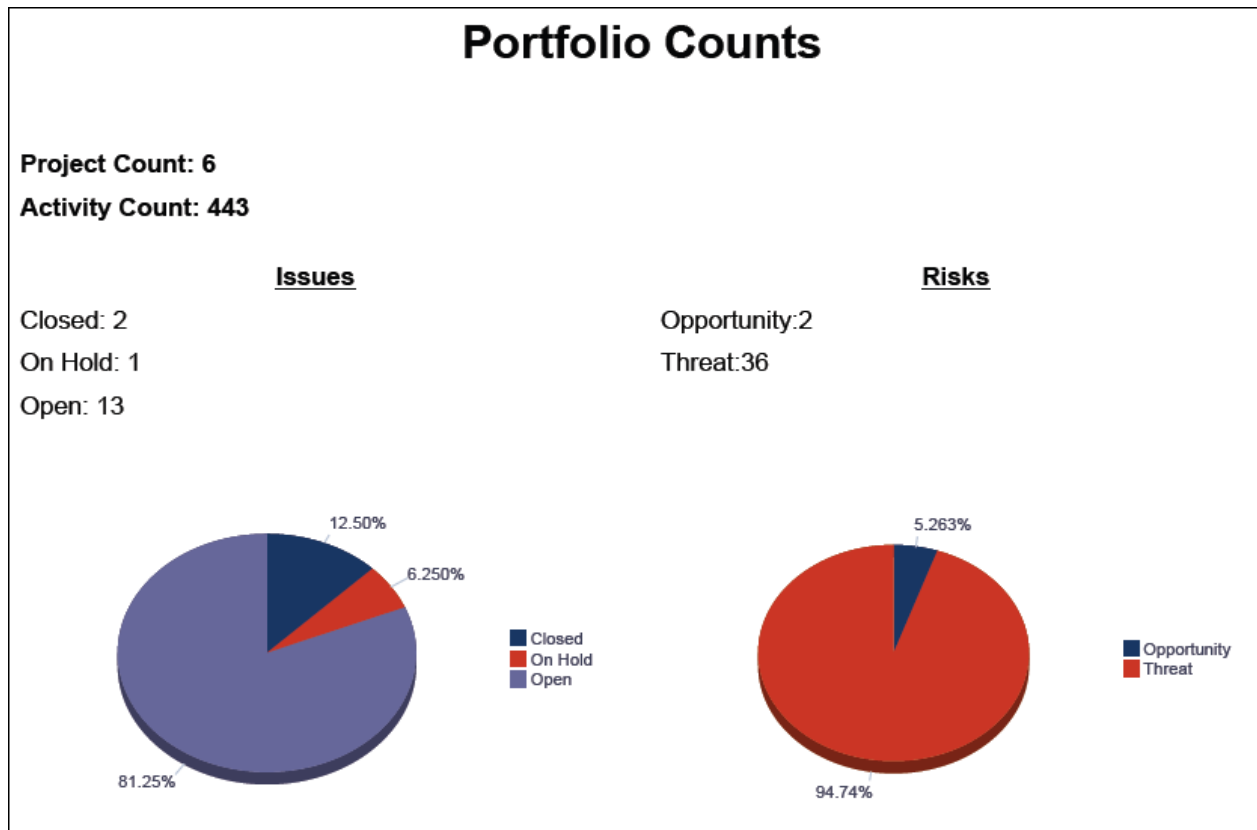

### Description

Provides a count of all projects and activities within the selected portfolio. In addition, two pie charts display the number of open and closed issues and risks.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Portfolio** folder.
  - d. Click **Portfolio Counts**.

## Project Portfolio Review

Figure 36: Project Portfolio Review

Project Portfolio Review					
Project(ID)	Project Manager	Project Location	Current Phase	Planned Start	Data Date
Harbour Pointe Assisted Living Center(EC00610)	Jones	Perth	Development	08/10/2014	09/27/2015
ISSUE		PRIORITY	STATUS		
Building 2 Subject To Delay		High	Closed		
Forecast Overrun		Top	Closed		
Unit Finishes Experiencing Productivity Delays		High	Closed		
RISK		STATUS	TYPE		
Concrete supply constrained		Closed	Threat		
Site access restricted for 2 weeks		Closed	Threat		
Weather delay due to hurricane		Closed	Threat		
Poor ground conditions		Closed	Threat		
Failed electrical inspection		Closed	Threat		
Interior design changes		Closed	Threat		
Contractor financial instability		Closed	Threat		
Permit delay		Closed	Threat		
Window manufacturing delay		Closed	Threat		
Weather delay due to unusually wet weather		Closed	Threat		
New roof coating cuts roof install time		Closed	Opportunity		
NOTEBOOK TOPIC		NOTEBOOK DESCRIPTION			
Recent Accomplishments		Recently past strucutral and traffic inspection. No weather delays in the past month allowed us to pull in finish date by a week. We successfully accomplisied some work that had risk identified. The risks did not occur and we can now release 100k in contingency			

### Description

Lists Issues, Risks and Notebook Topics within the selected portfolio, grouping by project. Includes Status and Priority of issues, Status and Type of risks, and project-level information.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.

- c. Expand the **Portfolio** folder.
- d. Click **Project Portfolio Review**.

## Project Reports

### Baseline Projects Summary

*Figure 37: Baseline Projects Summary*

Saratoga Senior Community							
Project Baselines							
NAME	DATE ADDED	CURRENT BUDGET	ORIGINAL BUDGET	CURRENT VARIANCE	ACTIVITY COUNT	PLANNED LABOR UNITS	PLANNED LABOR COST
Saratoga Senior Community - B	2/14/10 11:23 AM	\$4,700,000	\$4,700,000	(\$58,550,000.00)	132		
Saratoga Senior Community - B1	7/30/10 3:29 PM	\$4,700,000	\$4,700,000	(\$58,550,000.00)	132		

### Description

Lists all the baselines for a project and shows the Baseline name, Date Added, Current Budget, Original Budget, Current Variance, Activity Count, Planned Labor Units, and Planned Labor Cost.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Baseline Projects Summary**.

## Document Assignments

Figure 38: Document Assignments

Document Assignments			
Document Category			
Activity Name			
Detailed Design Specifications			
Assemble Technical Data for Heat Pump			
Document Title	Deliverable	Work Product	WBS Name
Design	N	N	Design and Engineering
Design Building Addition			
Document Title	Deliverable	Work Product	WBS Name
Design	N	N	Design and Engineering

### Description

Provides a list of all documents assigned to activities and WBSs within the specified project, grouped by Document Category.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Document Assignments**.



## Issues

Figure 39: Issues

Issues				
Status				
Issue	Project ID	Status	Priority	Criticality
Notes				
Open				
Building 2 Subject To Delay	EC00630 - B1	Open	High	High
This is an issue connected with productivity delays on Unit Finishes in Building 1. Building 2 first floor finishes are to be completed by the same subcontractor that is experience delays now. Recommend official correspondence to Finshes Subcontractor and consider augmenting crews in Building 2 to pick-up delay.				
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.3	EC00630 - B1	Open	High	High
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.4	EC00630 - B1	Open	High	High

### Description

Lists all Issues identified for the selected projects, grouped by Status. The issue details include Priority, Criticality, and issue description, if provided.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Issues**.

## Project Earned Value

### Description

Displays monthly Actual Cost, Earned Value, and Planned Value in both a bar chart along with a table for the selected projects.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:

- a. Click the **Reports** tab.
- b. Expand the **P6Reports** folder.
- c. Expand the **Project** folder.
- d. Click **Project Earned Value**.

---

## Project Earned Value and Issues - Monthly

### Description

Displays tables showing:

- ▶ Monthly and cumulative planned and actual earned value
- ▶ Monthly budget, forecast, and ETC
- ▶ Cumulative monthly budget, forecast, and ETC

And a bar chart of Earned Value as well as a list of issues for the selected projects, including the Issue Name, Activity ID, Status, Priority, creation date, and Description.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Project Earned Value and Issues - Monthly**.

---

## Project Earned Value by Date Range

### Description

Displays monthly Actual Cost, Earned Value, and Planned Value in a bar chart along with a table for the selected projects.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Project Earned Value and Issues - Monthly**.

## Project Plan Hierarchy

Figure 40: Project Plan Hierarchy

Project Hierarchy Including Steps				
WBS Code	WBS Code Name			
	Activity Name(ID)	Status	Start	Finish
Saratoga Senior Community - B3	Saratoga Senior Community - B3			
	Building Pad Delivered by Owner (EC1010)	Not Started	06/01/2011	06/01/2011
	Permits Received - Start Site Work (EC1080)	Not Started	06/01/2011	01/05/2015
	Substantial Completion - All TCO (EC2430)	Not Started	01/05/2015	01/05/2015
	<b>Landscape &amp; Irrigation</b>			
	Site Cleanup (EC1600)	Not Started	01/05/2012	03/20/2012
	Landscape & Irrigation (EC2360)	Not Started	10/04/2013	01/05/2015

### Description

Displays the project plan which lists all WBSs and activities for the selected project. The activity details include the Status, Start and Finish dates, and the associated activity Steps.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Project Plan Hierarchy**.

## Project Status Report

Figure 41: Project Status Report

Project Status Report for: Rural Office Building Addition (EC00515-1)

SPONSOR Forsyth	BUSINESS SEGMENT 1004050	PROJECT MANAGER Thomas	CURRENT PHASE Design	LOCATION Europe	
DESCRIPTION Project is for the addition to the office building in center city. This includes design and construct work.					
START 11/01/2010	FINISH 07/03/2013	TARGET FINISH 07/03/2013	% COMPLETE 17.07%	ACTIVITIES COMPLETED 13 of 71	PROJECT SCORE 80
APPROVED BUDGET \$2,064,211	COST TO DATE \$126,428	AT COMPLETION \$1,823,209	COST VARIANCE \$241,002	LABOR TO DATE 2062 h	LABOR VARIANCE 2331.6 h

PRIORITY ISSUES

0 priority of 0 issues

OPEN RISKS

0 open of 0 risks

NOTEBOOKS

MILESTONES

	Date	Status
Assemble Brick Samples	3/1/2011	Completed
Assemble and Submit Flooring Samples	3/1/2011	Completed
Begin Building Construction	3/1/2011	Completed
Begin Structural Phase	11/24/2011	Not Started
Building Addition Complete	7/3/2013	Not Started

### Description

Provides a project overview that includes project code values, project costs, Issues, Risks, Status of the milestones, and a list of Notebook Topics.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Project Status Report**.

## Qualitative Risk Report

Figure 42: Qualitative Risk Report

Project Summary					
Project ID	IT00351		Data Date		
Project Name	Project Swordfish		Finish		
Total Activities	15		At Completion Cost		
Completed	0		Actual Cost to Date	\$0	
In Progress	5		Remaining Total Cost		

Risk Summary					
Total Risks	7	Threats	7	Opportunities	0
Risks by Status					
Proposed	0	Closed (Impacted)	0		
Open	6	Closed (Managed)	0		
Active	1	Closed (Rejected)	0		

Risks by Tolerance Threshold			
High	Medium	Low	Negligible
3	2	2	0

ID	NAME				
Risk-01	Technological Complexity				
Type: Threat	Category: Complexity & Interfaces		Status: Open	Owner: CharlesM	
Impacted Activities					
Activity (ID)	Early Start	Early Finish	Actual Start	Actual Finish	
Develop System (IT1060)	06/10/2011	07/08/2011			
Test System (IT1070)	07/07/2011	07/18/2011			

Pre-Response Assessment		Score: 9	
Probability	Schedule	Cost	
High(H)	High(H)	High(H)	

### Description

Reports on all risks for the select projects. Includes risk information, Risk Impact Assessment, Impacted Activities, and Risk Response Plans.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.

- d. Click **Qualitative Risk Report**.

---

## Risk Contingency Drawdown

### Description

Displays risk contingency drawdown.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Risk Contingency Drawdown**.

---

## Risk Exposure

### Description

Displays risk exposure.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Risk Exposure**.

## Risk Scoring

Figure 43: Risk Scoring

Project Summary

Project ID: MFG00772

Project Name: Cordova - Plant Expansion & Modernization

Total Activities: 134

Completed: 51

In Progress: 4

Data Date: 04/30/2011

Finish: 05/29/2012

At Completion Cost: \$1,258,004

Actual Cost to Date: \$436,491

Remaining Total Cost: \$821,513

Risk Summary

Report Date: 10/08/2010

Total Risks: 6

Threats: 5

Opportunities: 1

Proposed Risks: 1

Open Risks: 1

Active Risks: 2

Rejected (Closed): 1

Managed (Closed): 1

Impacted (Closed): 0

Risk by Tolerance Threshold

Very High	High	Low	Very Low	Negligible
1	1	2	2	0

Probability

Very Low	Low	Medium	High	Very High
<=10%	>10%	>30%	>50%	>70%

Impacts

	Very Low	Low	Medium	High	Very High
Schedule	<=40	>40	>80	>160	>320
Cost	<=\$30,000.00	>\$30,000.00	>\$60,000.00	>\$90,000.00	>\$120,000.00
Quality Threshold (5 level)	Substantially meeting the specification	Sufficiently meeting the specification	Non-conformance in minor systems	Non-conformance in major functional systems	Non-conformance in critical systems

Tolerance

Very Low	Low	High	Very High
<=3	>3	>10	>24

Probability and Impact Scoring (PID)

Risk Score is based on: Highest Impact

Impact


	Severity 1	Severity 2	Severity 3	Severity 4	Severity 5
Very High	12	24	42	56	72
High	5	14	20	36	56
Medium	4	6	18	20	42
Low	2	4	6	14	24
Very Low	1	2	4	5	12

Key

Very High	High	Low	Very Low
>24	>10	>3	<=3

## Risk Scoring

Figure 44: Risk Scoring (v2)

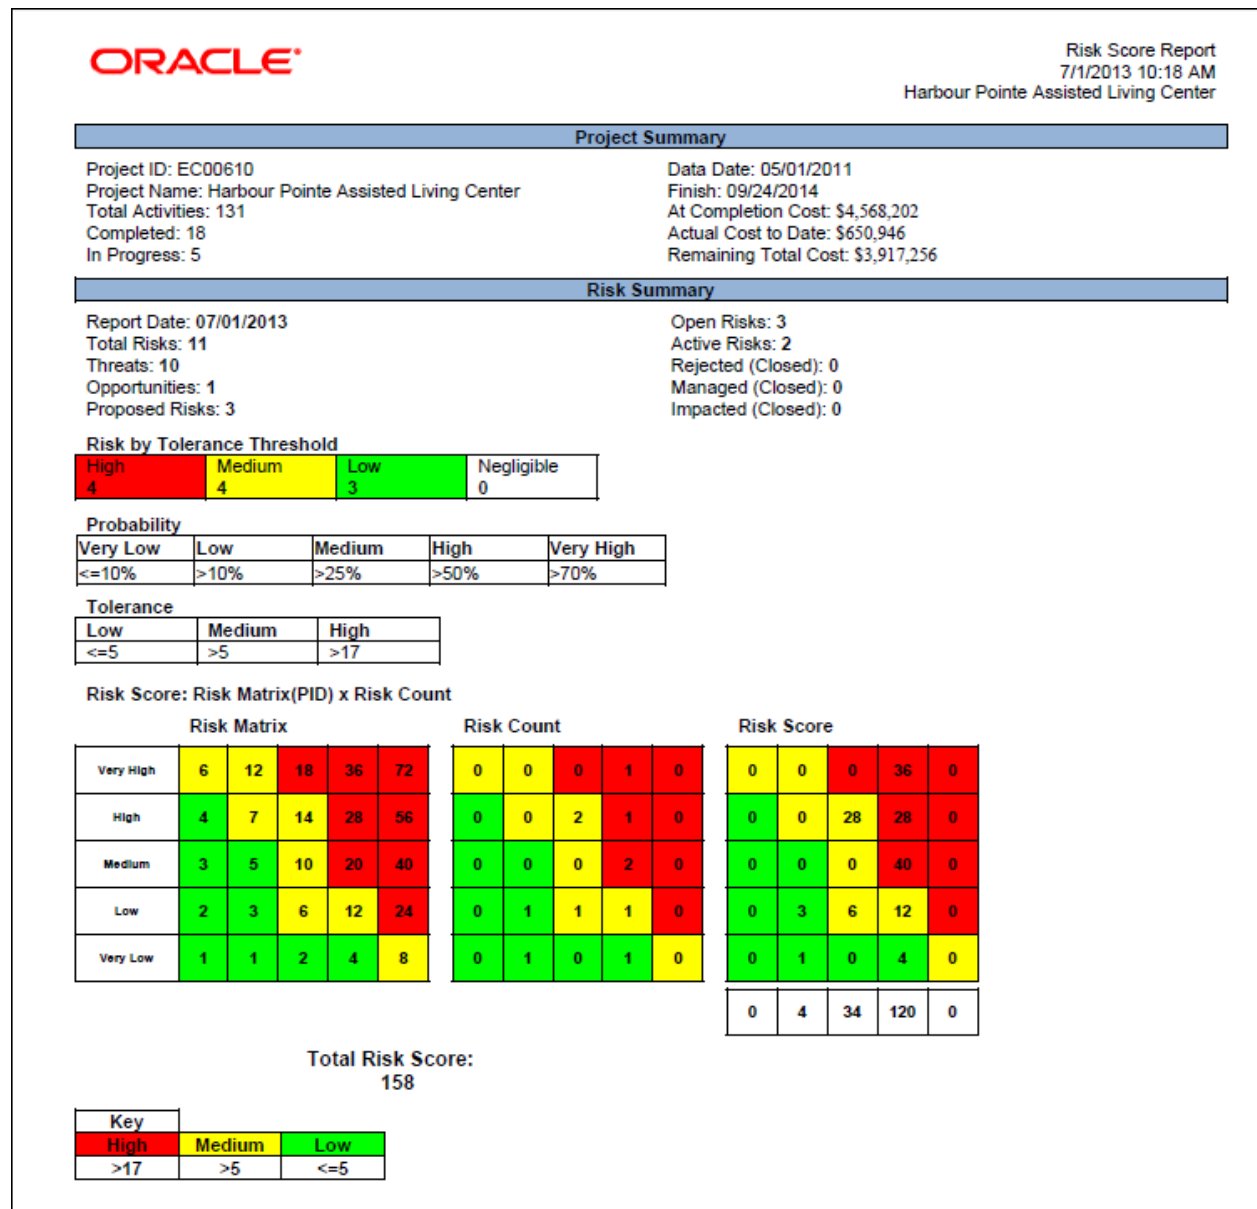

## Risk Scoring (v2)

### Description

Choose which version of the report to run from **Template**.

Risk Scoring shows the project risk scoring matrix. Includes threshold definitions grouped by type (Probability, Schedule, Cost, User-defined, and Tolerance) and numeric and alphanumeric probability and impact diagrams (PIDs).




Risk Scoring (v2) shows project risk scoring matrix. Includes threshold definitions grouped by type (Tolerance Threshold, Probability and Tolerance), PIDs for Risk Matrix, Risk Count and Risk Score and Total Risk Score.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **Risk Scoring**.

## S Curve

Figure 45: S Curve

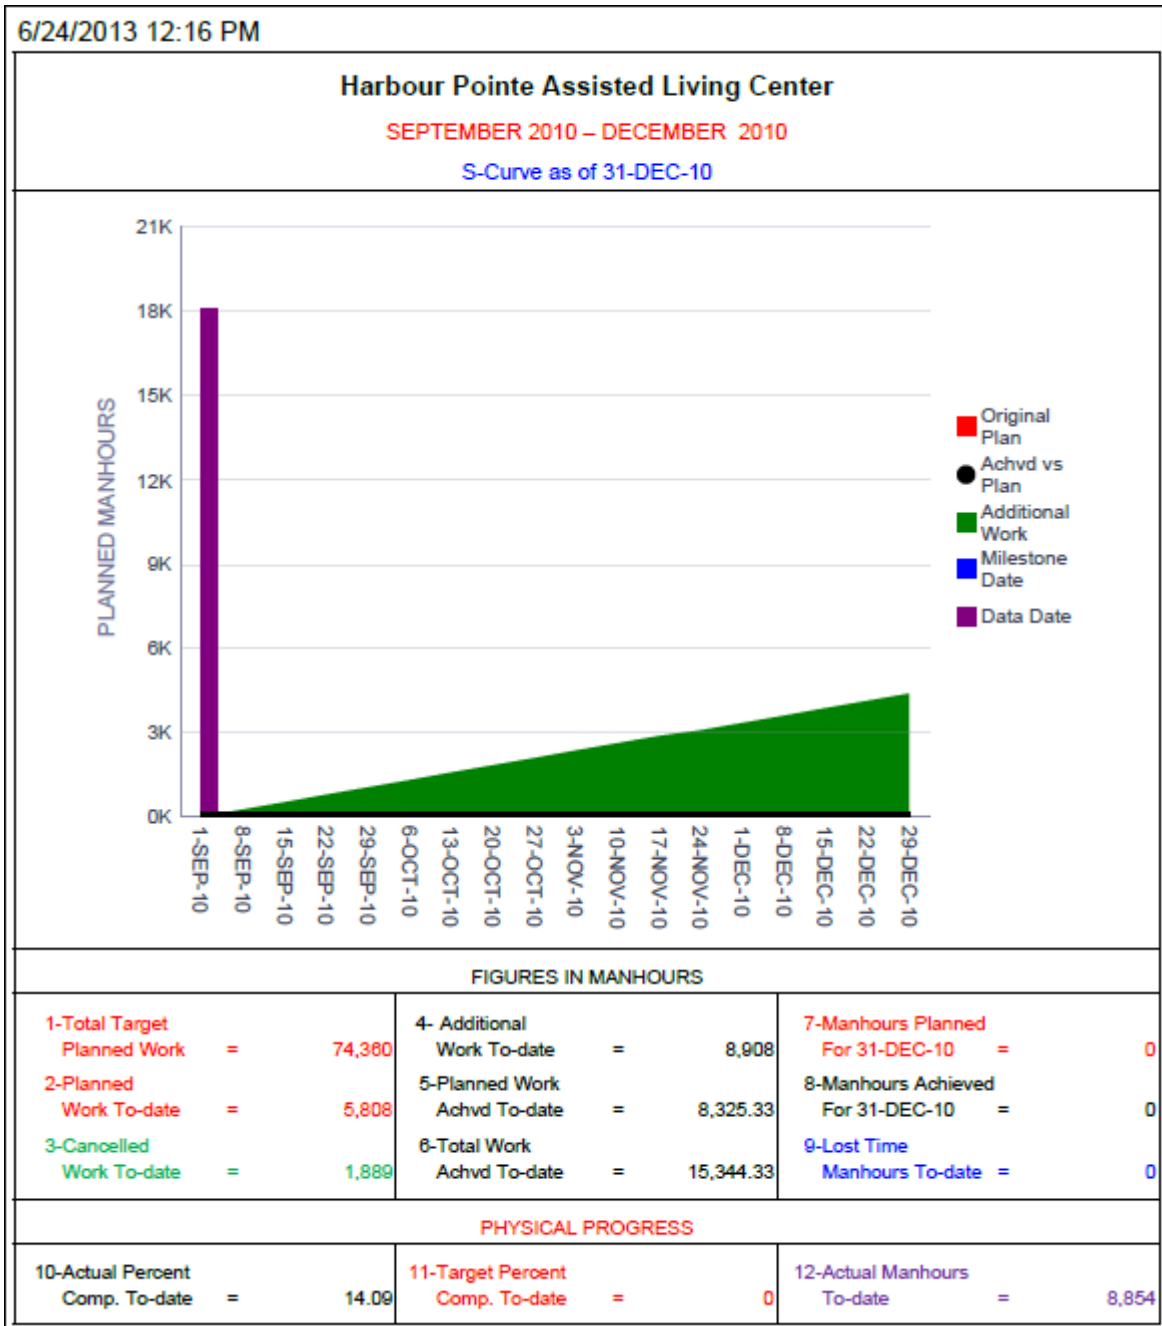

## Description

This report consists of a chart and a table. The chart shows Planned Labor Units on the y-axis and date on the x-axis and plots the Original Planned Labor Units, Achieved versus Plan, Additional Work and Milestone Dates. The table gives the Total Target Planned Work, Planned Work To Date, Cancelled Work To Date, Additional Work To Date, Planned Work Achieved To Date, Total Work Achieved To Date, Manhours Planned, Manhours Achieved, Lost Time Manhours To Date, Actual Percent Complete To Date, Target Percent Complete To Date, and Actual Manhours To Date.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Project** folder.
  - d. Click **S Curve**.

## Weekly Schedule Performance

Figure 46: Weekly Schedule Performance

Weekly Schedule Performance												
Logistics Reengineering Program												
	9/5/2010			9/12/2010			9/19/2010			9/26/2010		
	Actual	Planned	%	Actual	Planned	%	Actual	Planned	%	Actual	Planned	%
Start	2	2	100	2	2	100	1	1	100	0	0	0
Finish	1	1	100	3	3	100	0	1	0	0	0	0
Assisted Living Facility												
	9/5/2010			9/12/2010			9/19/2010			9/26/2010		
	Actual	Planned	%	Actual	Planned	%	Actual	Planned	%	Actual	Planned	%
Start	12	12	100	0	0	0	1	1	100	0	0	0
Finish	3	3	100	0	0	0	0	0	0	1	1	100

## Description

Compares the activity Actual Finish date to the Baseline Finish date. Activities are grouped by week and project. The report will display information starting four weeks prior to the date set in the report parameters.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.

- b. Expand the **P6Reports** folder.
- c. Expand the **Project** folder.
- d. Click **Weekly Schedule Performance**.

## Resource Reports

### Activity Resource Assignments

Figure 47: Activity Resource Assignments

Activity Resource Assignments																			
Activity (ID)	Duration	Start	Finish																
Design Building Addition (EC1000)	417.6	11/01/2010	01/19/2011																
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>441.6</td><td>11/01/2010</td><td>01/19/2011</td></tr> <tr> <td>Scott Esposito</td><td>417.6</td><td>11/01/2010</td><td>01/19/2011</td></tr> <tr> <td>Scott Esposito</td><td>417.6</td><td>11/01/2010</td><td>01/19/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	441.6	11/01/2010	01/19/2011	Scott Esposito	417.6	11/01/2010	01/19/2011	Scott Esposito	417.6	11/01/2010	01/19/2011
Resource Name	Duration	Start	Finish																
Paul Kim	441.6	11/01/2010	01/19/2011																
Scott Esposito	417.6	11/01/2010	01/19/2011																
Scott Esposito	417.6	11/01/2010	01/19/2011																
Start Office Building Addition Project (EC1010)	0	11/01/2010	11/01/2010																
Review and Approve Designs (EC1030)	86.4	01/17/2011	02/17/2011																
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>86.4</td><td>01/17/2011</td><td>02/17/2011</td></tr> <tr> <td>Scott Esposito</td><td>86.4</td><td>01/17/2011</td><td>02/17/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	86.4	01/17/2011	02/17/2011	Scott Esposito	86.4	01/17/2011	02/17/2011				
Resource Name	Duration	Start	Finish																
Paul Kim	86.4	01/17/2011	02/17/2011																
Scott Esposito	86.4	01/17/2011	02/17/2011																

### Description

Lists resources assigned to each activity in the selected projects. Information includes Start and Finish dates along with Duration.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Activity Resource Assignments**.

## FTE (headcount)

### Description


Display full time employee headcount.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **FTE (headcount)**.

## Limit Line

Figure 48: Limit Line

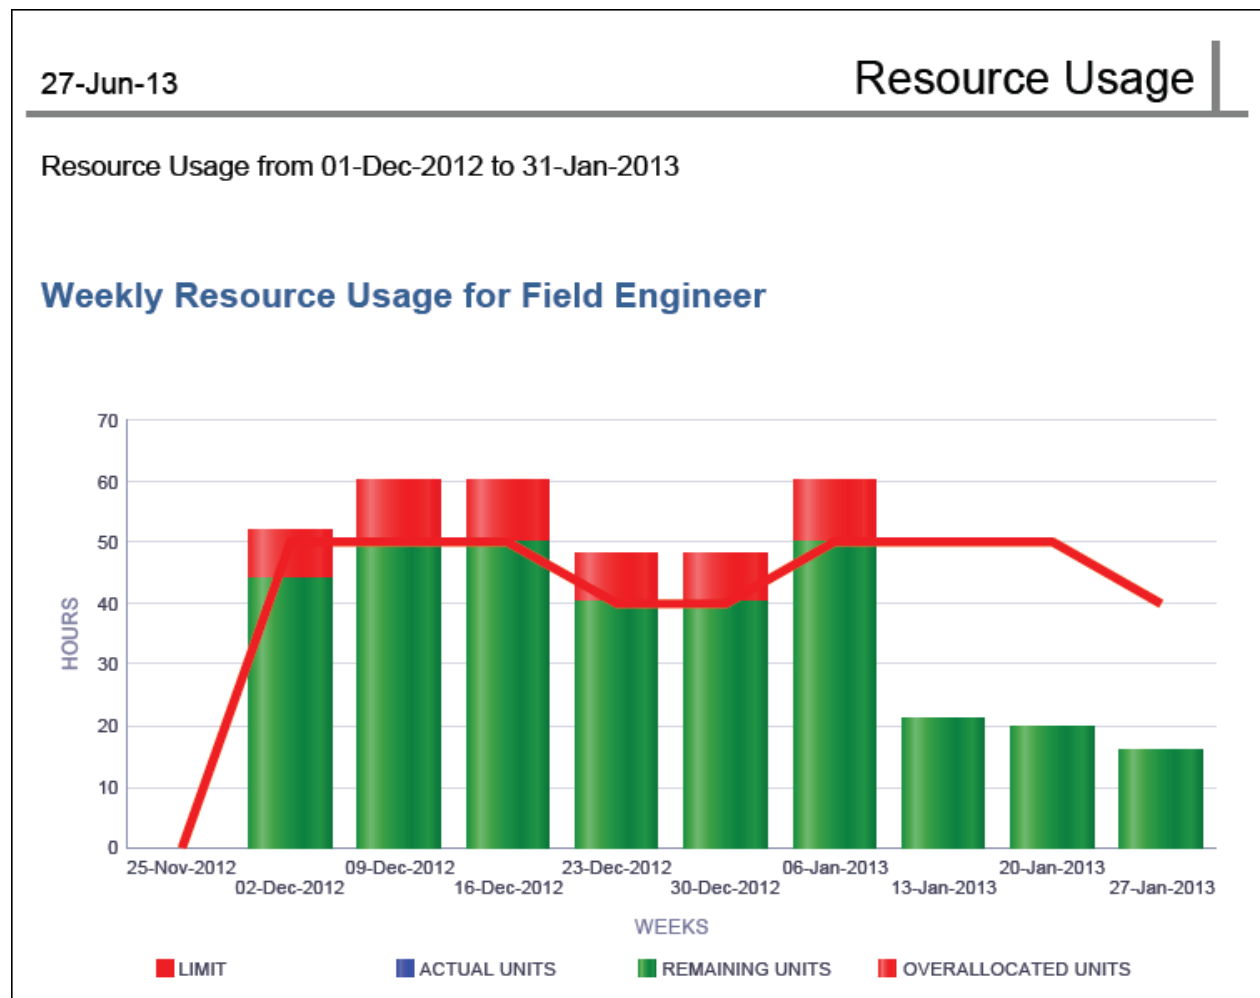

## Description

A bar-line graph for each resource showing bars for Actual Units, Remaining Units, and Overallocated Units and a line for the resource's Limit. The y-axis shows hours. The x-axis shows week.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Limit Line**.

## Resource Code Assignments

Figure 49: Resource Code Assignments

Resource Code Assignments		
Resource Code		
	Code Value	Resource Name
Classification	CONTR	Gary Marshall
		Conveying Subcontractor
		Roofing Subcontractor
		Utilities Subcontractor
		BPM Consultant 1
		Millwork Subcontractor
		Thermal Protection Subcontractor
		Finishes & Fit-out Subcontractor
		Fire Suppression Subcontractor

## Description

Displays a list of all Resource Codes and Resource Code Values along with the resources assigned to each code value.

## Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Resource Code Assignments**.

## Resource Role Associations

Figure 50: Resource Role Associations

Resource Role Associations		
Role (count)		
Resource (ID)	Proficiency	Primary Role
<b>Process Architect (5)</b>		
Judy Billings (BillingsJ)	3 - Skilled	Yes
Frank Chu (Chuf)	2 - Expert	Yes
Wayne Prescott (PrescottW)	3 - Skilled	Yes
Michelle Peterson (PetersonM)	4 - Proficient	No
Ben Frost (FrostB)	2 - Expert	No
<b>Accounting (2)</b>		
Project Controls (Project Controls)	3 - Skilled	No
Administrator (Admin)	3 - Skilled	No

### Description

Displays a list of all roles in the system and the resources assigned to each role. The Primary Role and Proficiency level are identified for each resource.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Resource Role Associations**.

## Resource Role Skill Sets

Figure 51: Resource Role Skill Sets

Resource Role Skill Sets			
Resource (Role count)			
	Role	Primary Role	Proficiency
<b>Painter (1)</b>			
	Trades	Yes	3 - Skilled
<b>Project Managers (1)</b>			
	Management	Yes	3 - Skilled
<b>Alice Wynn (2)</b>			
	Product Tester	Yes	3 - Skilled
	Lean Six Sigma Specialist	No	3 - Skilled

### Description

Lists all resources along with their assigned roles. The Primary Role and Proficiency level are identified for each role.


### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Resource Role Skill Sets**.



## Resource Stacked Histogram

Figure 52: Resource Stacked Histogram

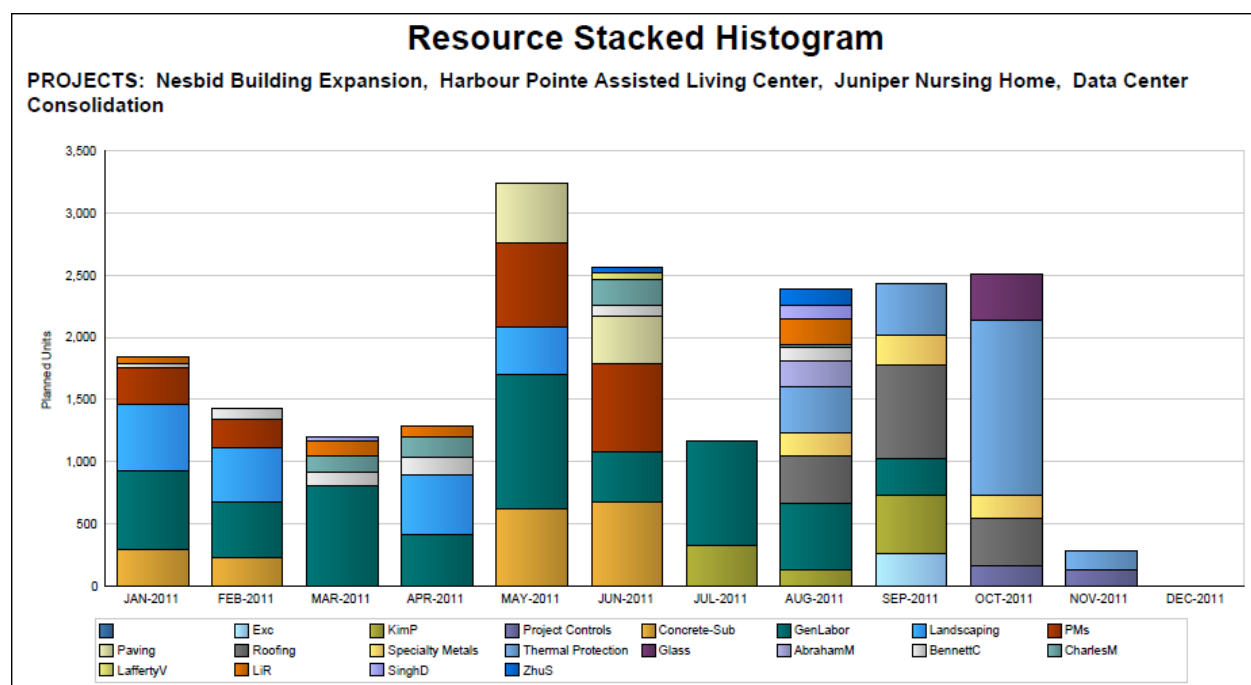

### Description

Displays a stacked histogram that shows effort as Planned Units (in hours) for selected resources, stacking bars by resource within the start and end date ranges.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.
  - b. Expand the **P6Reports** folder.
  - c. Expand the **Resource** folder.
  - d. Click **Resource Stacked Histogram**.

## Role Code Assignments

### Description

Displays a list of role code assignments.

### Location

- 1) Click **Reports**.
- 2) On the **Report** page:
  - a. Click the **Reports** tab.

- b. Expand the **P6Reports** folder.
- c. Expand the **Resource** folder.
- d. Click **Role Code Assignments**.

## About Publication Services

---

Before you can generate reports or view data in some areas of P6, data must be refreshed and calculations must be made in precisely arranged tables and fields. *Publication Services* address these needs, gathering and calculating data as close as possible to real-time. To make this happen, you can configure P6 to publish data to specific tables used for these features. An administrator must configure settings for Publication Services before you can publish data. For reports, depending on the type of data published, P6 tables may still be used to generate reports, or a combination of P6 and reporting tables may be used to generate them.

Your organization's P6 EPPM published data has two categories: *project* data and *global* data.

- ▶ **Published project data** includes all information about your projects, including aggregates, calculations, and auditing data. Most pages that use published data use published project data.

You can publish project data on an ad-hoc basis using the Publish Projects item on the Actions menu of the EPS or Activities pages, allow P6 to publish automatically on the basis of how much the project has changed, or you can schedule a service to publish project data automatically.

- ▶ **Published global data** includes enterprise data for projects (for example, codes and UDFs), activities (for example, codes and UDFs), resources, and calendars as well as the enterprise data dictionary and security data. Reports use published global data as well as published project data.

Global data is published by services which are usually scheduled to run automatically.

P6 tracks all projects enabled for publishing and determines when each project will be published on the basis of the number of changes made to the project and the time since its data was last published. You can configure the settings guiding this process on the Services page of Application Settings.

- ▶ **Publish a changed project when the... Number of changes exceeds:** P6 tracks the combined number of changes to the project itself as well as its WBS, activities, relationships, resource and role assignments, risks, project codes, activity codes, and UDFs.
- ▶ **Publish a changed project when the... Time since last publication exceeds:** P6 also considers when the project was most recently published and whether that period exceeds the Time since last publication setting.

If both the number of changes is great enough and the published data is old enough, as stipulated by these two settings, P6 creates a job to publish the data.


---

**Note** P6 has checks in place to ensure that publishing jobs cannot impair system performance, no matter how many jobs are created at any given time.

---

## Working with Publication Services

To achieve near real-time reporting, usage, and analysis date, you can configure P6 to publish to tables that store updated data, including calculations and summary data. These tables also create views for generating reports. The P6 data is split into two general categories: *project* data and *global* data. Project data includes all information about your projects, including aggregates and calculations. Global data includes enterprise data, as well as resource and role, portfolio, and security data. The image below encapsulates the key concepts in the publication and reporting process.

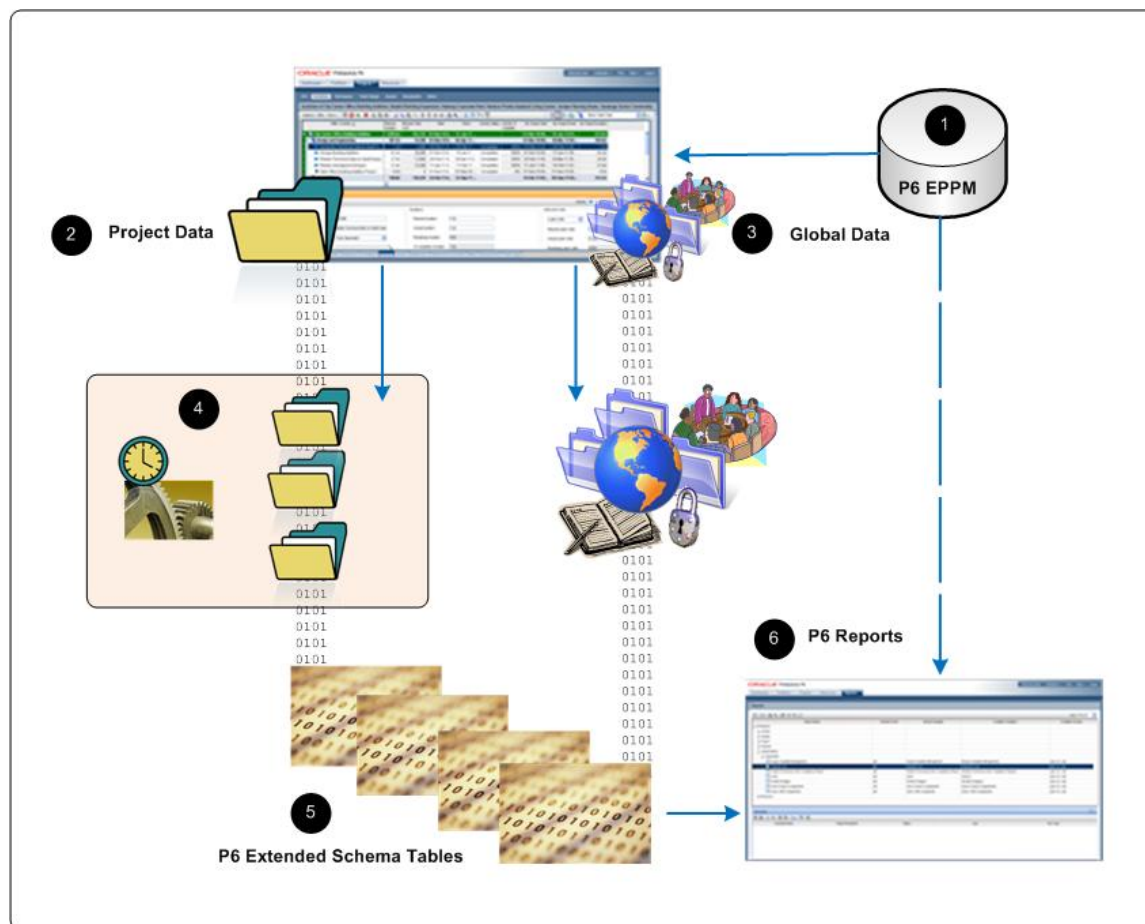

**Table of Key Publication Services Concepts**

Item	Description
①	<b>EPPM Database:</b> The EPPM database captures all the data your organization generates every second of every day. However, the raw data in the EPPM database is not structured for immediate reporting.
②	<b>Project Data:</b> You can configure P6 to publish a project based on publication thresholds. Based on the options you select, you can prioritize projects for publication in a queue. If necessary, you can manually add a project to the queue.

Item	Description
3	<b>Global Data:</b> You can configure services in P6 to schedule the publication of global data based on recurring intervals that you specify. If necessary, you can also immediately publish this data manually.
4	<b>Project Queue:</b> Projects publish in sequential order based on priority. Your administrator can control which projects are added to the publishing queue, when, and in what order. These options ensure the project data you need most is available for P6 in near real-time.
5	<p><b>P6 Extended Schema Tables:</b> The project and global services recalculate certain logical fields in the P6 EPPM database and store them as physical fields in the P6 Extended Schema tables so they are available for reporting and other purposes. Some fields in P6, such as durations, are calculated in real time as related field data is changed and are not stored in the database. Publication services recalculate these fields and store their values in the extended schema tables. Other fields, such as notebook topics, are not stored in the database in a format suitable for reporting. For these fields, publication services will convert them to a format more suitable for reporting.</p> <p><b>Note</b> For information about which tables are updated by the Publication Services, see the following knowledge management document: What PX tables are updated when running Global Scheduled Services or Publish Project (KB495991)</p>
6	<b>P6 Reports:</b> You can run reports directly against P6 Extended Schema table views.

## Configuring Publication

Before data can be published, you must configure the settings that control publishing in P6.

- 1) Specify the timeframe for which data should be published and the distribution interval for the published data.  
See **Defining Publication Periods** (on page 86).
- 2) Enable publication and specify how often data will be published.  
See **Enabling Automatic Publishing of P6 Project Data** (on page 87).
- 3) Determine the types of enterprise and project data to publish.  
See **Enabling Automatic Publishing of P6 Global Data** (on page 88).
- 4) Specify which projects should be published and the relative priorities of projects for publishing.  
See **Configuring Publication Service Settings for Projects** (on page 89).
- 5) Optionally set up services to publish project data at scheduled intervals.  
See **Creating Project Scheduled Services** (on page 90).

## Publishing P6 Data

Reports based on P6 data require timely access to the most current data in order to be accurate. For example, report recipients expect to see updated enterprise data and project data including any calculations.

Some other areas of P6 also rely on published data to provide accurate information.

In order to provide this data, P6 generates and stores data in reporting tables (the *P6 Extended Schema*). You can configure P6 to publish essential data to the tables automatically, schedule the publication of project data to happen at specific times of day, or you can choose to generate it on demand so that the most current data is available. You can select to be notified by email if publication services fail.

The data is split into two general categories: *project* data and *global* data. Project data includes all information about your projects, including baselines, summaries, calculations, and audit data. Global data includes enterprise data, project, activity, resource, calendar, enterprise data dictionary, resource and role data, security and audit data. Most pages that use published data access project data. Reports can use both project and global data.

---

**Note** In areas of the software that show published data, a user who has the right to view costs and financials at WBS level but not at Project level will not see financial data at the WBS level. Although the user has the privilege to view cost and financial data at WBS level, the data is only published at project level.

---

## Publication Services

Data in the P6 Extended Schema is calculated and stored by Publication Services, which gives administrators control over when data is calculated and stored in the P6 Extended Schema. Publication Services exist for project and global data. Global data includes enterprise data, as well as resource and role, portfolio, security and audit data. Project data includes all information about projects and baselines, including summaries and calculations.

The Publish Project service is dedicated to publishing project and baseline data to the P6 Extended Schema.

---

**Note** The Publish Project service recalculates and publishes all project business objects containing calculated or denormalized data including, but not limited to: the WBS, activities, resource/role assignments, high-level planning assignments, relationships, risks, documents, expenses, steps, milestones, UDF values, notes, issues, budget change logs, timesheets, code assignments, funding source assignments.

---

These additional Publication Services publish global data to the P6 Extended Schema:

- ▶ Publish Audit Data
- ▶ Publish Enterprise Data
  - ▶ Project Data
  - ▶ Activity Data

- ▶ Resource Data
- ▶ Calendar Data
- ▶ Enterprise Data dictionary definitions
- ▶ Publish Enterprise Summaries
- ▶ Publish Resource Management
- ▶ Publish Security

The first time a data type is published to the P6 Extended Schema all data is recalculated and published to the extended schema tables. After a data type has been published for the first time, future publication services recalculate and publish only data that has changed since the last time that data was published.

When any of the publication services runs, each business object type processed by the service is individually timestamped, and the timestamp stored in the database. The services can accurately determine exactly which data has changed since the last time it was published using these timestamps because they exist at the individual business object type level.

Configure Publication Services in P6 as follows:

- ▶ Set up automatic publication and enable P6 to publish project and global data on the Services page in Application settings.
- ▶ Enable the types of global data to be scheduled in Global Scheduled Services.
- ▶ Disable or enable publication for a selected project on the Services page in Project Preferences.
- ▶ Add, verify the status of, modify, or delete project management services on the Project Scheduled Services page.

**Tip**

Run the global data services before turning on the Project Arbiter service.

## Defining Publication Periods

Before publishing global or project data for reporting, define the publication period. The publication period you define should be large enough to capture all the project data you need to include in reports. Data before or after the defined publication period range is assigned to the period before or after the publication period range (respectively).


---

**Caution** You can perform these steps again at any time to modify your settings. However, if an *Admin Superuser* modifies the Start date, Time distributed interval, or Finish date is current date plus fields, all data will be fully recalculated. Oracle recommends that you only reconfigure publication options on weekends or during off-peak hours to prevent the disruption of other P6 features.

---

To define the publication period:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Application Settings**.

- 3) On the **Application Settings** page, click **Services**.
- 4) On the Services page, in the Publication Periods section:
  - a. In the **Start date** field, click  **Select Date** to select the exact month, day, year, and time to mark the initial start of the data publication period. Select any date in the past that represents a reasonable amount of historical spread data for your organization. For example, in order for users to be able to produce time-distributed reports for any date range, enter the earliest project start date at your organization.
  - b. In the **Finish date is current date plus** field, select a numeric quantity and unit of time to construct a dynamic period of time. Whenever a publication service runs, this period of time is added to the current date to determine the finish date for the publication of data. For example, if the value is 5 years, time-distributed data will always be published covering the period of time that begins with the value in the Start Date field and extends five years into the future each time a service runs.
  - c. In the **Time distributed interval** field, select the unit of time in which time distributed data will be recalculated and published. Time distributed interval is set to Week by default. Set this to Day if you need to see daily data.
  - d. Click **Save**.

### Enabling Automatic Publishing of P6 Project Data

Perform the following procedure to enable projects for publication, and to set options for automatic project publication. Then, as you work, P6 automatically detects the changes to your projects that trigger the publication of their data.

To enable Publication Services for project data:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Application Settings**.
- 3) On the Application Settings page, select **Services**.
- 4) On the Services page, in the Project Publication section:
  - a. Select **Enable Publish Projects** to enable automatic project publication based on defined thresholds. Selecting this option also allows users to publish projects on demand.
  - b. In the **Publish projects every** field, select an interval by which projects are polled to be published.
  - c. Enter a number in the **Number of changes exceeds** field. This threshold setting determines the number of edits users can make to the project data before P6 publishes its data. Assuming a constant rate of change among projects, a lower value will result in more frequent publication of project data. If you enter a value of 0, projects with tracked changes will be automatically published.
  - d. Enter a time period for the **Time since last publication exceeds** field. This threshold setting determines how often the publication of project data should occur. For example, if you enter 12 hours, the project data will be published every 12 hours unless the threshold for the number of changes has already been reached.
  - e. Select **Publish idle projects** to add projects to the service queue that are enabled for publication but have not been changed during the time threshold. This setting is only valid for the initial run of the service.



- f. In the **Maximum number to publish** field, enter the maximum number of pending idle *Publish Project* services that can be present at once in the service queue. This prevents performance problems during peak demand when enabling the publication of a large number of projects. For example, if the service runs and queues 40 projects that have exceeded specified thresholds and must be published, or that have been published on demand by users, and you have set the maximum to 100, P6 will schedule up to 60 idle projects for publication.
- g. Select **Publish resource and role data** if you want to be able to publish resource and role spread data.
- h. Select **Enable Baseline Publication** if you want to be able to publish baseline data.
- i. Select **Enable Notification Email** and type an email address in the **Notification Email address** field if you want to receive an email if publication services fail.
- j. Click **Save**.

**Tip**

- ▶ You can also schedule project data to be published at specific times of day.
- ▶ If your organization is upgrading to P6, select Publish idle projects to add your migrated projects to the service queue after your database is upgraded. This will publish all your projects in the queue and refresh the available data for reporting. After an upgrade, this setting is no longer applicable, and projects will be submitted to the service queue based on threshold values specified on the Application Settings page.
- ▶ Clear the Publish idle projects option if your organization does not report against completed projects.
- ▶ The Maximum number to publish field is only applicable immediately following an upgrade, when all projects are considered idle. When all projects have been published, the service queue will no longer be constrained based on this setting.
- ▶ A project will be automatically submitted to the service queue if you change the project baseline, calendar, or data date. Projects are also automatically submitted to the queue if you select or clear Calculate Activity % Complete from activity steps option, or modify the default price/unit value for assignments without activities, from the Set Project Preferences dialog box.
- ▶ For threshold settings, projects are added to the service queue based on tracked changes to data. Only changes to activities, resource/role assignments, relationships, risk assignments, UDF values, activity code assignments, project code assignments and the WBS are tracked.
- ▶ You can delete published project data by selecting **Delete Published Data** on the **Actions** ▾ menu of the EPS page.

### Enabling Automatic Publishing of P6 Global Data

Perform the steps below to configure P6 to automatically publish any of the following types of global data to reporting tables.

- ▶ Enterprise Data
  - ▶ Project Data
  - ▶ Activity Data
  - ▶ Resource Data



- ▶ Calendar Data
- ▶ Enterprise Data dictionary definitions
- ▶ Enterprise Summary Data including portfolio data
- ▶ Resource Management Data
- ▶ Security Data
- ▶ Audit Data

To automatically publish P6 global data:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Scheduled Services**.
- 3) On the Scheduled Services page, select **Global**.
- 4) On the Global page:
  - a. Select a service, then configure its settings in the Service Settings detail window. For example, you might specify that the service runs daily with a start time of 08:00 AM.


**Note** Oracle recommends running the Publish Security service first if the Run After Previous option is selected in the Run Service list for other publication services. Running the Publish Security service first will ensure that security data updates in the extended schema as soon as possible and ensures that the security restrictions are in place before you run the report.

- b. Select the **Enabled** option for any of the global services listed.
- c. If you choose to run one or more services with the relative frequency value of *After previous service*, click **Move Up** or **Move Down** to arrange the services in your preferred sequence.
- d. Click **Save**.

## Configuring Publication Service Settings for Projects

After enabling automatic publishing or adding a job to publish project data on a scheduled basis, perform the following procedure to configure settings for each individual project in *Publication Services*. Then, as you work, P6 automatically detects the changes to your project that trigger the publication of its data in the service queue.

To configure Publication Service settings for a project:

- 1) Click **Projects**.
- 2) On the Projects navigation bar, click **EPS**.
- 3) On the **EPS** page:
  - a. Select a project.
  - b. Click  **Row Actions** and select **Set Project Preferences**.
  - c. In the Project Preferences dialog box, select **Analytics & Services**.
  - d. On the Analytics & Services page, in the Publication section:
    - Select the **Enable Publication** option.

- Adjust the relative **Publication Priority** up or down between 1 and 100 with 50 being the default priority value, 1 being the highest priority, and 100 being the lowest.
- e. Click **OK**.

**Tip**

- ▶ By default, all projects are enabled for publication. You only need to modify the Enable Publication setting if you want to disable publication for a project or re-enable publication of a previously disabled project.
- ▶ Clearing the Enable Publication setting does not delete previously published data. You can delete published project data by selecting Delete Published Data on the **Actions** ▾ menu in the EPS page.
- ▶ If you wish to modify publication settings for many projects at one time, you can display the Enable Publication, Last Published On, and Publication Priority fields as columns in your EPS view.
- ▶ If you want to publish Baseline data, you must also publish project data for the relevant projects.

## Creating Project Scheduled Services

You can schedule services to run at intervals you choose on projects that you select. Available services include apply actuals, export, import, level, project checker, publish, schedule, summarize, and send to schedule sheet.

To create project scheduled services:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Scheduled Services**.
- 3) On the Scheduled Services page, click **Project**.
- 4) Click **Add** ▾ and select the type of service to add.
- 5) Enter a name for the new service.
- 6) In the Project Settings detail window:
  - a. Select **+ Add** to add projects, EPS nodes, project code values, or portfolios to the Project table.

---

**Note** You cannot select projects for Import Primavera XML services.

---

- b. Enter or select a value for every field.
- 7) Select or clear the **Enabled** option to determine whether the service will run.
- 8) Select **Save**.

**Tip**

You cannot schedule services for project templates.

## Configuring Publication Service Settings for Baselines

After enabling automatic publishing or adding a job to publish project data on a scheduled basis, perform the following procedure to configure settings for each individual project's baselines in Publication Services. Then, as you work, P6 automatically detects the changes to your baselines that trigger the publication of its data in the service queue.

To configure Publication Service settings for a baseline:

- 1) Click the **Projects** ▾ menu and choose **Open Projects**.
- 2) In the **Open Projects** dialog box, open one or more projects whose baselines you want to enable for publication.
- 3) On the **Project** navigation bar, click **Activities** or **EPS**.
  - a. On the Activities or EPS page, click **Actions** ▾ and select **Define Baselines**.
  - b. In the Define Baselines dialog box:
    - If you want to switch on publication for all baselines for a project, select the **Publish** option in the project band.
    - If you want to switch on publication for only some baselines for a project, expand the project band and select the **Publish** option for the baselines you want to publish.
    - Click **Save**.

## Publishing P6 Project Data On Demand

You can publish the data from projects on demand. Projects are added to the queue of projects being processed for publication the next time the Publish Projects service runs. You can check the status of the Publish Projects service after it has been added to the service queue by selecting View Service Status from the User menu. When you publish projects on demand, any of the projects' baselines which is enabled for publishing will also be published. Only projects enabled for publication are published.

To publish P6 project data on demand:

- 1) Click **Projects**.
- 2) On the Projects navigation bar, click **EPS**.
- 3) On the EPS page:
  - a. On the **Actions** ▾ menu, click **Publish Projects**.

### Tip

- ▶ In order to manually project data from the EPS page on demand, *Publication Services* must be enabled and configured.
- ▶ You can publish all open projects by clicking Publish Projects on the **Actions** ▾ menu of the Activities page. You can also publish projects by selecting one or more projects on the EPS page, and then using the right-click menu.
- ▶ If you have permission to view application settings, you can see the settings for the Publish Projects service, including how often the service runs, on the Global tab of the Scheduled Services page.

- ▶ A project will be automatically submitted to the service queue if you change the project baseline, calendar, or data date. Projects are also automatically submitted to the queue if you select or clear the Calculate Activity % Complete from activity steps option, or modify the default price/unit value for assignments without activities from the Set Project Preferences dialog box available from the **Actions** ▾ menu the EPS page.
- ▶ You can delete published project data by selecting **Delete Published Data** on the **Actions** ▾ menu of the EPS page.

### Publishing P6 Global Data On Demand

You can publish any of the following types of global data to the reporting tables on demand.

- ▶ Enterprise Data
  - ▶ Project Data
  - ▶ Activity Data
  - ▶ Resource Data
  - ▶ Calendar Data
  - ▶ Enterprise Data dictionary definitions
- ▶ Enterprise Summary Data including portfolio data
- ▶ Resource Management Data
- ▶ Security Data
- ▶ Audit Data

To publish P6 global data on demand:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Scheduled Services**.
- 3) On the Scheduled Services page, select **Global**.
- 4) On the Global page:
  - a. Select a global service.
  - b. Click **Run Service**.
  - c. In the resulting message box, click **OK**.

#### Tip

- ▶ If the service listed under the manually selected service is configured to run After previous service, it will run automatically when the selected service finishes.
- ▶ You must have the *Administer Global Scheduled Services* global security privilege to run a global scheduled service.

### Deleting Published P6 Project Data

In Standard View, perform the steps below to delete published project data. This is useful when you no longer need to report on projects which are completed, but you need to retain the projects in your database.

To manually delete P6 global data:

- 1) Click **Projects**.

- 2) On the Projects navigation bar, click **EPS**.
- 3) On the EPS page:
  - a. On the **Actions** ▾ menu, click **Delete Published Data**.

**Tip**

- ▶ You need the xxx privilege assigned
- ▶ This process is for Oracle databases only.

## Supported Parameters in P6

You can use any parameter for reports, but users will have to ensure they enter the value correctly, or the SQL statements in the data template will fail. Using supported parameters will allow you to provide a user interface to enter the values for parameters. Supported parameters for P6 fall into one of three categories:

- ▶ **Enumeration** parameters allow users to pick parameters from static lists.
- ▶ **Dynamic** parameters will generate the list at run time. For example, when focusing on Project ID, users will see a project list that pulls the current projects from the P6 EPPM database.
- ▶ **Primitive** parameters support basic selections. For example, if a parameter is a boolean, an option will appear for users to select or clear a text box instead of typing true or false.

The following are the supported parameters for P6, grouped by category:

### Enumeration Parameters

- ▶ Activity Priority
- ▶ Assignment Proficiency
- ▶ Activity Status
- ▶ Activity Type
- ▶ Constraint Type
- ▶ Duration Type
- ▶ Percent Complete Type
- ▶ Project Status
- ▶ Rate Source
- ▶ Rate Type
- ▶ Resource Type
- ▶ Risk Status
- ▶ Risk Type

### Dynamic Parameters

- ▶ Activity Code Value
- ▶ User Defined Activity Code (type and value)
- ▶ Cost Account
- ▶ EPS
- ▶ Expense Category
- ▶ Funding Source

- Portfolio
- Project
- Project Code Value
- User Defined Project Code (type and value)
- User Defined Resource Code
- Resource Code Value
- Resource Team
- Resource ID
- Responsible Manager
- Risk Category
- Role
- Role Team
- Timesheet Period
- User

### Primitive Parameters

- Date
- Boolean
- Integer
- Float

### Custom Parameters

- List of Values

## Enumeration Parameters

Enumeration parameters map to fields that have a set list of possible values. When running a report with a enumeration parameter, P6 will offer a list to select one of the values. Users will see the localized text for the enumeration value's description; however, the return value will be the English description of the enumeration, which is the value the PX Views database stores.

This section contains the following information for each supported enumeration parameter:

- **Identifier:** The value you must enter in the identifier field in BI Publisher when creating the parameter for the report.
- **Details:** A description and technical details of the parameter.
- **Values:** The values that will be available in P6.
- **Maps to field:** The database field the return value maps to in the PX Views database. It could match multiple fields in the database, so only the primary table is listed.
- **Use case:** An example of how you might use the parameter in a report.

The following enumeration parameters are supported:

### Parameter: Activity Priority

- **Identifier:** p\_activity\_priority

- **Details:** Allows users to select the leveling priority of an activity.
- **Values:** Top, High, Normal, Low, Lowest
- **Maps to field:** ACTIVITY.LEVELINGPRIORITY
- **Use case:** Filter activity data by leveling priority.

#### Parameter: Assignment Proficiency

- **Identifier:** p\_assignment\_proficiency
- **Details:** Allows users to select a value for assignment proficiency.
- **Values:** Master, Expert, Skilled, Proficient, Inexperienced
- **Maps to field:** RESOURCEASSIGNMENT.PROFICIENCY
- **Use case:** Filter resource assignment data by the proficiency of the assignment.

#### Parameter: Activity Status

- **Identifier:** p\_activity\_status
- **Details:** Allows users to select activity status.
- **Values:** Not Started, In Progress, Completed
- **Maps to field:** ACTIVITY.STATUS
- **Use case:** Filter activity reports based on a certain status.

#### Parameter: Activity Type

- **Identifier:** p\_activity\_type
- **Details:** Allows users to select the activity type.
- **Values:** Task Dependent, Resource Dependent, Level of Effort, Start Milestone, Finish Milestone, WBS Summary
- **Maps to field:** ACTIVITY.TYPE
- **Use case:** Filter activity reports based on the type of the activity.

#### Parameter: Constraint Type

- **Identifier:** p\_constraint\_type
- **Details:** Allows users to select an activity constraint type.
- **Values:** Start On, Start On or Before, Start On or After, Finish On, Finish On or Before, Finish On or After, As Late As Possible, Mandatory Start, Mandatory Finish
- **Maps to field:** ACTIVITY.PRIMARYCONSTRAINTTYPE and ACTIVITY.SECONDARYCONSTRAINTTYPE
- **Use case:** Filter activities in a report by the activity primary or secondary constraint type.

#### Parameter: Duration Type

- **Identifier:** p\_duration\_type
- **Details:** Allows users to select the duration types of an activity.
- **Values:** Fixed Units/Time, Fixed Duration & Units/Time, Fixed Units, Fixed Duration & Units
- **Maps to field:** ACTIVITY.DURATIONTYPE

- **Use case:** Filter activities in a report based on their duration type.

#### Parameter: Percent Complete Type

- **Identifier:** p\_percent\_complete\_type
- **Details:** Allows users to select the percent complete type of an activity.
- **Values:** Physical, Duration, Units
- **Maps to field:** ACTIVITY.PERCENTCOMPLETETYPE
- **Use case:** Filter activities in a report based on the percent complete type of the activity.

#### Parameter: Project Status

- **Identifier:** p\_project\_status
- **Details:** Allows users to select the status of a project.
- **Values:** Planned, Active, Inactive, What If, Requested, Template
- **Maps to field:** PROJECT.STATUS
- **Use case:** Filter the projects in a report based on the desired type. For example, you might want to use this for a report that needs to display information only on planned projects.

#### Parameter: Rate Source

- **Identifier:** p\_rate\_source
- **Details:** Allows users to select the rate source of an assignment.
- **Values:** Resource, Role, Override
- **Maps to field:** RESOURCEASSIGNMENT.RATESOURCE
- **Use case:** Filter resource assignments included in a report based on the rate source of the assignment.

#### Parameter: Rate Type

- **Identifier:** p\_rate\_type
- **Details:** Allows users to select the rate type of an assignment.
- **Values:** Price/Unit, Price/Unit 2, Price/Unit 3, Price/Unit 4, Price/Unit 5
- **Maps to field:** RESOURCEASSIGNMENT.RATETYPE
- **Use case:** Filter resource assignments included in a report based on the rate type of the assignment.

#### Parameter: Resource Type

- **Identifier:** p\_resource\_type
- **Details:** Allows users to select the resource type of an assignment.
- **Values:** Labor, Nonlabor, Material
- **Maps to field:** RESOURCEASSIGNMENT.RESOURCE TYPE
- **Use case:** Filter resource assignments included in a report based on the resource type of the assignment.



**Parameter: Risk Status**

- **Identifier:** p\_risk\_status
- **Details:** Allows users to select the status of a risk.
- **Values:** Proposed, Open, Active, Rejected (Closed), Managed (Closed), Impacted (Closed)
- **Maps to field:** RISK.RISKSTATUS
- **Use case:** Filter risks in a report based on the status of the risk.

**Parameter: Risk Type**

- **Identifier:** p\_risk\_type
- **Details:** Allows users to select the type of a risk.
- **Values:** Threat, Opportunity
- **Maps to field:** RISK.RISKTYPE
- **Use case:** Filter risks in a report based on the type of risk.

**Dynamic Parameters**

Dynamic parameters map to fields that have a varying list of possible values. When running a report with a dynamic parameter, P6 will offer a list to select one of the available values.

This section contains the following information for each supported dynamic parameter:

- **Identifier:** The value you must enter in the identifier field in BI Publisher when creating the parameter for the report. In some cases, identifiers can pass in context by appending short names to the end of the identifier. The character in quotations is the separator that the code splits and <name> represents the context you are trying to pass in.
- **Details:** A description and technical details of the parameter.
- **P6:** What the editor for the parameter will be in the Reports section of P6.
- **Return Value:** The values that will be available in P6.
- **Maps to field:** The database field the return value maps to in the PX Views database. It could match multiple fields in the database, so only the primary table is listed.
- **Use case:** An example of how you might use the parameter in a report.

The following dynamic parameters are supported:

**Parameter: Activity Code Value**

- **Identifier:** p\_a\_code\_val\_\_<short name>
- **Details:** Enables users to select an activity code value via a list. Context passes into the parameter by appending a colon":" followed by the short name of the activity code type you want to set.
- **P6:** Provides a list that displays the Activity Code Values for the Activity Code type passed in the context.
- **Return value:** Short name of the Activity Code (unique per code type).
- **Maps to field:** ACTIVITYCODE.CODEVALUE

- ▶ **Use case:** Create a report that displays some basic information about activities. Users at five locations need to run the report, but they only want to see the data for activities with codes matching their location. Instead of creating five reports hard coding the location (for example, location=L1) on each report, you can create one report and add this parameter to it (for example, p\_a\_code\_val\_\_Location).

In the data template for the report, filter the activities based on this parameter. Hard code the left side of the activity filter to match the activity code you selected, which in this case is location.

**Example query:** CODETYPENAME='Location' &  
CODEVALUE=:p\_a\_code\_val\_\_Location

If you did not have a parameter for this, you would need different templates for each location.

### Parameter: User Defined Activity Code

- ▶ **Identifier:** p\_activity\_code\_value "." <number> p\_activity\_code\_type "." <number>
- ▶ **Details:** Enables users to select a user defined Activity Code. The user defined Activity Code is two parameters on the report in BI Publisher, but will display only as one row in the report settings parameter table.
- ▶ **P6:** Provides a list that displays all global Activity Code types. When users expand a type, the list shows the values for that type. By selecting a value, both the type and value will return to the report.
- ▶ **Return value:** Short name for the Activity Code Value, primary key for the Activity Code type.
- ▶ **Maps to field:**
  - p\_activity\_code\_value maps to ACTIVITYCODE.CODEVALUE
  - p\_activity\_code\_type maps to ACTIVITYCODE.CODETYPEOBJECTID
- ▶ **Use case:** Create a report that can have a variable Activity Code. The report pulls activities and displays some basic statistics of the activities. The data template for the report must accommodate setting both sides of the query. While a typical parameter just sets the IN clause for a user defined field, this parameter must set both sides. The "Activity Code Value" parameter **Use case** example shows where it hard codes the CODETYPENAME to be **Location**. This parameter enables multiple user defined activity codes to be used on the same report. For each parameter you use, you must add p\_activity\_code\_value.1 and p\_activity\_code\_type.1. There must be a pair of numbers to ensure that the editor works properly.

### Parameter: Cost Account

- ▶ **Identifier:** p\_cost\_account
- ▶ **Details:** Enables users to select Cost Accounts. The P6 user must have access to view Cost Accounts for the list to populate.
- ▶ **P6:** Provides a list that displays all Cost Accounts in a hierarchical tree.
- ▶ **Return value:** Short name of the cost account (unique).
- ▶ **Maps to field:** COSTACCOUNT\_FULL.NAME
- ▶ **Use case:** Filter items using certain Cost Accounts or generate information on the Cost Accounts.

**Parameter: EPS**

- **Identifier:** p\_eps\_id
- **Details:** Enables a user to select an EPS.
- **P6:** Provides a list that displays all of the EPS nodes where the user has access.
- **Return value:** The short name of the EPS.
- **Maps to field:**
  - EPS\_FULL.NAME
  - EPS\_U.NAME
- **Use case:** Use a parameter for EPS to filter a query to load all projects under an EPS for a report.

**Parameter: Expense Category**

- **Identifier:** p\_expense\_category
- **Details:** Enables a user to select Expense Category where the user has access.
- **P6:** Will provide a list that displays all of the Expense Categories.
- **Return value:** The short name of the Expense Category (unique).
- **Maps to field:**
  - EXPENSECATEGORY\_FULL.NAME
  - EXPENSECATEGORY\_U.NAME
- **Use case:** Run a report filtered by assignments that use a certain Expense Category associated with them.

**Parameter: Funding Source**

- **Identifier:** p\_funding\_source
- **Details:** Enables a user to select a Funding Source.
- **P6:** Provides a hierarchical list filled with Funding Sources where a user has access.
- **Return value:** The short name of the Funding Source (unique).
- **Maps to field:**
  - FUNDINGSOURCE\_FULL.NAME
  - FUNDINGSOURCE\_U.NAME
- **Use case:** Filter the report data to include only projects that have the selected Funding Source assigned.

**Parameter: Portfolio ID**

- **Identifier:** p\_portfolio\_id
- **Details:** Enables a user to select a Portfolio where the user has access.
- **P6:** Provides a list of Portfolios where the user has access.
- **Return value:** The portfolio short name (unique).
- **Maps to field:** PROJECTPORTFOLIO\_FULL.NAME
- **Use case:** Filter the report data to include only the projects in a Portfolio.

---

**Note** If there is a user portfolio that shares the same name as one of the global portfolios, then the report will return data for both when you run it. You'll need to use the Portfolio Name and User ID to make a unique constraint.

---

#### Parameter: Project ID

- ▶ **Identifier:** p\_project\_id
- ▶ **Details:** Enables a user to select one or more projects where the user has access.
- ▶ **P6:** Click the Projects \_ menu, and select **Open Project** to display the Project list. Enables switching between Template and Regular projects.
- ▶ **Return value:** The project short name (unique).
- ▶ **Maps to field:** PROJECT\_FULL.ID
- ▶ **Use case:** Run a report where the data comes from selected projects.

#### Parameter: Project Code Value

- ▶ **Identifier:** p\_p\_code\_val\_\_<short name>
- ▶ **Details:** Select a Project Code value. Note that underscores (\_) are the only special character allowed. Do not use other special characters.
- ▶ **P6:** Provides a list containing the project code values for the Project Code whose short name matches the second part of the parameter. For example: If the short name was Scope, and there were four values – Local, Regional, Country, and Global – the list would display Local, Regional, Country, and Global in the list.
- ▶ **Return value:** Activity code value short name (unique per code type).
- ▶ **Maps to field:** PROJECTCODE\_FULL.CODEVALUE
- ▶ **Use case:** Filter the set of projects loaded to those projects that have the user-selected Project Code Value assigned to them.

#### Parameter: User Defined Project Code

- ▶ **Identifier:** p\_project\_code\_value"."<number> p\_project\_code\_type"."<number>
- ▶ **Details:** Similar to the User Defined Activity Code, this parameter consists of two parameters in BI Publisher: One parameter returns the selected Project Code Value, and the other parameter returns the Project Code type ID. For each parameter you use, you must add both **p\_project\_code\_value.#** and **p\_project\_code\_type.#**. There must be a pair of numbers for the editor to work properly. You can have multiple sets to allow for more than one User Defined Code Value.
- ▶ **P6:** Provides a list populated with all the global Project Codes as the first level. Expanding a Project Code type will list all the values for the type. In the parameter table, only one row will represent both parameters. After you select a Project Code Value, both parameters will be set.
- ▶ **Return value:** The short name for p\_project\_code\_value and the object id for p\_project\_code\_type.
- ▶ **Maps to field:**
  - p\_project\_code\_value maps to PROJECTCODE\_FULL.CODEVALUE

- p\_project\_code\_type maps to PROJECTCODE\_FULL.CODETYPEOBJECTID
- ▶ **Use case:** Create a report that enables the projects to filter based on a Project Code that the user defines. Unlike the Project Code Value parameter, the report creator should not hard code the Project Code type. Instead, they should write the query to enable the p\_project\_code\_type.1 parameter to determine the Project Code type. This lets a report be more flexible in the filter criteria.

### Parameter: User Defined Resource Code

- ▶ **Identifier:** p\_resource\_code\_value "." <number> p\_resource\_code\_type "." <number>
- ▶ **Details:** Similar to the other user-defined codes this parameter consists of two parameters on the report in BI Publisher: One parameter returns the selected Resource Code Value, and the other parameter returns the Resource Code type ID. For each parameter you use, you must add both **p\_resource\_code\_value.#** and **p\_resource\_code\_type .#**. There must be a pair of numbers in order for the editor to work properly. You can have multiple sets to allow for more than one user-defined code value.
- ▶ **P6:** Provides a list populated with the Resource Codes as the first level. Expanding a Resource Code type will list all the values for the type. In the parameter table, only one row will represent both parameters. After you select a Resource Code Value, both parameters will be set.
- ▶ **Return value:**
  - p\_resource\_code\_value: short name for the code value
  - p\_resource\_code\_type: object id for the code type
- ▶ **Maps to field:**
  - p\_resource\_code\_value maps to RESOURCECODE\_FULL.CODEVALUE
  - p\_resource\_code\_type maps to RESOURCE\_CODE\_FULL.CODETYPEOBJECTID
- ▶ **Use case:** Create a report that allows for the resources to be filtered based on a Resource Code Value and type that the user defines. Unlike the Resource Code Value parameter, the report creator should not hard code the resource code type. Instead, they should write the query to enable the p\_resource\_code\_type.1 parameter to determine the resource code type. This allows a report to be more flexible in the filter criteria.

### Parameter: Resource Code Value

- ▶ **Identifier:** p\_r\_code\_val\_\_<short name>
- ▶ **Details:** Select a Resource Code value to use for filtering loaded resources for a report.
- ▶ **P6:** Provides a list populated with the resource code values for the resource code type indicated by the <short name> at the end of the parameter. For example: If the short name was Department, the list would display Engineering, Marketing, Research, and Development as the values in the list.
- ▶ **Return value:** The short name of the Resource Code Value (unique per code type).
- ▶ **Maps to field:** RESOURCECODE\_FULL.CODEVALUE

- **Use case:** Create a report where the resources filter based on the resources that match the user-selected Resource Code Value for a particular Resource Code type. The report data query must hard code the Resource Code type for matching resources to the returned code value.

#### Parameter: Resource Team

- **Identifier:** p\_resource\_team
- **Details:** Enables resource team selection.
- **P6:** Provides a list populated with resource teams that the user has access to view.
- **Return value:** The short name of the resource team (unique).
- **Maps to field:** RESOURCETEAM\_FULL.NAME
- **Use case:** Filter a report to load resources that are on the selected resource team.

#### Parameter: Resource ID

- **Identifier:** p\_resource\_id
- **Details:** Select a resource to filter a report.
- **P6:** Provides a list populated with resources that the user has access to view.
- **Return value:** The short name of the resource (unique).
- **Maps to field:** RESOURCES\_FULL.NAME
- **Use case:** Filter the activities in a report based on the user-selected resource assigned to the activity.

#### Parameter: Responsible Manager

- **Identifier:** p\_responsible\_manager
- **Details:** Select a responsible manager (OBS).
- **P6 GUI:** Provides a list populated with the OBS structure that the user has access to view.
- **Return value:** The short name of the OBS (unique).
- **Maps to field:** PROJECT\_FULL.OBSNAME and OBS\_FULL.NAME
- **Use case:** Filter a report to load only the projects that have the user-selected responsible manager.

#### Parameter: Risk Category

- **Identifier:** p\_risk\_category
- **Details:** Select a Risk Category.
- **P6:** Provides a list populated with all the Risk Categories that the user has access to view.
- **Return value:** The name of the Risk Category (unique).
- **Maps to field:** RISK\_FULL.RISKTYPE
- **Use case:** Filter a report to load only the Risks of the user-selected category.

#### Parameter: Role Team

- **Identifier:** p\_role\_team

- **Details:** Select a Role Team.
- **P6:** Provides a list populated with all the Role Teams the user has access to view.
- **Return value:** The name of the Role Team (unique).
- **Maps to field:** ROLLTEAM\_FULL.NAME
- **Use case:** Filter a report of Resources to include only the Resources that are assigned to the user-selected Role Team.

#### Parameter: Role

- **Identifier:** p\_p6\_role\_id
- **Details:** Select a Role.
- **P6:** Provides a list populated with all the Roles the user has access to view.
- **Return value:** The short name of the Role (unique).
- **Maps to field:** ROLL\_FULL.ID
- **Use case:** Filter a report of Resources to include only the Resources that have the user-selected Role.

#### Parameter: Timesheet Period

- **Identifier:** p\_timesheet\_period\_start and p\_timesheet\_period\_end
- **Details:** This parameter consists of two parameters on the report in BI Publisher, but is represented by a single row in parameter list for P6. The user will select a timesheet period, and it will set the Start Date to p\_timesheet\_period\_start and the End Date to p\_timesheet\_period\_end.
- **P6:** Drop down menu of the Timesheet Periods in the database. Selecting a Timesheet Period will return the Start Date and End Date in the parameters.
- **Return value:** The Start Date and End Date of the Timesheet Period selected by the user.
- **Maps to field:** N/A
- **Use case:** Filter a report to look for a date between two dates of a Timesheet Period. Instead of adding two date parameters and making the user manually enter the Start and End of the period, the user can use a drop down with the Timesheet Periods in the database.

#### Parameter: User

- **Identifier:** p\_p6\_user\_id
- **Details:** Select a P6 EPPM user name.
- **P6:** Provides a list populated with the P6 users that the logged-in user has access to view.
- **Return value:** The user name (unique).
- **Maps to field:** USERS\_FULL.NAME

## Primitive Parameters

In BI Publisher, when you create a parameter, a field Data Type allows the following options: String, Integer, Boolean, Float. The default type is String, and you should use it for all supported enumeration and dynamic parameters. For primitive parameters, select the appropriate option for the parameter that you are configuring.

### Type: Date

- ▶ **Editor:** P6 will use the date picker to select the date.
- ▶ **Return:** The date string in the format entered in BI Publisher.

### Type: Boolean

- ▶ **Editor:** Will use a check box editor.
- ▶ **Return:** Either true (selected) or false (cleared).

### Type: Integer

- ▶ **Editor:** Will use a default text box without validation.
- ▶ **Return:** The text entered in the box.

### Type: Float

- ▶ **Editor:** Will use a default text box without validation.
- ▶ **Return:** The text entered in the box.

## Allowing for Multiple Values Returned via a List

If you need a supported parameter to return a comma separated list of values for an IN clause in the data template, do the following:

- 1) In BI Publisher, set the parameter type to **Menu**. This will allow you to link it to a list.
- 2) Create a hard-coded list or a query to get the possible values for the parameter.  
See examples of this in BI Publisher's pre-packaged reports.
- 3) Select the list of values you just created for the parameter.
- 4) Check the **Multiple Selection** option for the parameter.

If a parameter allows for multiple selection, P6 allows selection of multiple values from the list or allows users to continue to assign values without closing the list. When the return value appears, parameter values are comma-delimited.



## About Table Auditing

Table auditing helps you to determine what changes have been made at a table level in the database. You can log changes made to each table regardless of who made the change or when the change was made. You can then run reports on audited data. Two sample reports are available.

---

### Note

- You must configure auditing before any data will be captured against which you can run reports.
  - Table auditing involves an increased amount of interaction between P6 and the database, which can affect performance.
  - **Cloud Only:** To collect audit data on BLOB fields, submit a Service Request in My Oracle Support. See: ***How To Retrieve PAUDIT Audit Data From Audit-Enabled Tables With A Blob Field Column Type (KB529380)***  
<https://support.oracle.com/support/?kmExternalId=KB529380>
- 

## Configuring Audit Settings

Configure Auditing in P6 so that you can produce reports about incremental changes to projects and project related data. You can view audit data collected by this process on the Audit panel of the EPS page, or by running reports to retrieve audit data from the database. See: *P6 EPPM Reporting Guide*.

---

**Note** Table auditing involves an increased amount of interaction between P6 and the database, which can affect performance.

---

To configure Auditing:

- 1) Click **Administration**.
- 2) On the Administration navigation bar, click **Application Settings**.
- 3) On the Application Settings page, click **Audit**.
- 4) On the Audit page:
  - a. In the **Interval to store user login information (in days)** field, enter a number of days.
  - b. In the **Interval to store audit information (in days)** field, enter a number of days.
  - c. In the Select the tables and operations to audit list, select a table or operation to audit and click **Add**.
  - d. In the Audit Tables section:
    - Select **Audit Insert** to audit insertions to the table.
    - Select **Audit Update** to audit updates to data in the table.
    - Select **Audit Delete** to audit deletions of data in the table.

### Note

- Select **Audit Insert** to see when new rows have been added to that table. For example, auditing inserts on the PROJECT table will show you when someone has created a new project.
- Select **Audit Update** to see when data in a table has been edited. For example, auditing updates on the PROJECT table will show you when someone has changed the name or other properties of a Project.
- Select **Audit Delete** to see when data in a table has been deleted. For example, auditing deletes on the PROJECT table will show you when someone has deleted a project.

e. Select **Enable auditing for all tables**.

5) Click **Save**.

### Tip

- ▶ Table auditing records data about changes to projects and project related data items to the PAUDIT table. To be able to view audit data, you must also configure and enable the Publish Audit Data service.
- ▶ To stop auditing on a particular table, remove it from the list by selecting **✕ Remove**, or by clearing all three audit options for that table.
- ▶ If you need to suspend all auditing without changing the configuration of the actions and tables which will be audited, clear the **Enable auditing for all tables** option.

About This Guide.....	3
About Personal Information .....	3
About Reports .....	3
Reporting in P6 EPPM (Cloud only) .....	4
Assigning Permissions for P6 EPPM Reporting (Cloud only) .....	5
Working with Reports .....	6
Scheduling Reports .....	7
Running Reports On-Demand.....	8
Viewing the Report Run History .....	9
Sample P6 EPPM Reports.....	10
Activity Reports.....	19
Activities That Can Work .....	19
Activity Look Ahead .....	20
Activity Relationships .....	21
Calendar.....	22
Cross Project Relationships .....	23
Duration Analysis.....	24
Schedule Report with Notebooks .....	25
Administrative Reports.....	26
Audit .....	26
Audit Data - All .....	26

Audit Data - Project.....	27
Approvals .....	28
Status Reviews - Pending.....	28
Status Reviews - Not Approved.....	29
Timesheets .....	30
Timesheets with Detailed Hours.....	30
Timesheets Report - Resource Manager.....	31
Timesheet Compliance.....	31
Timesheets Status with Notes .....	32
Timesheets Status without Notes .....	33
Timesheets Report - Project Manager.....	34
Activity Code Assignments - EPS .....	35
Activity Code Assignments - Global .....	36
Activity Code Assignments - Project.....	37
Global Calendar Use.....	38
Never Logged Users .....	39
Profile Privileges .....	39
Project Calendar Use.....	40
Project Governance Non-Compliance Report .....	41
Project Template Management .....	42
User Inactivity Report .....	43
User Inactivity Report - Active Users Only .....	44
User Login Report.....	45
User Login Report - Active Users Only .....	46
Users .....	47
Users - Active Users Only.....	48
Users OBS Assignments.....	49
Users Project Assignments .....	50
Industry Samples.....	51
Utilities .....	51
Online .....	51
Discrepancy Report .....	51
High Risk Look Ahead .....	52
T-Week Hit List.....	53
T-Week Look Ahead .....	54
Weekly Resource Loading.....	55
Outage.....	56
Critical Path Report .....	56
Outage Look Ahead .....	57
Variance Report.....	58
Portfolio Reports.....	59
Code Assignments.....	59
Investment Alignment Chart .....	60
Portfolio Counts .....	61
Project Portfolio Review .....	62
Project Reports.....	63

Baseline Projects Summary .....	63
Document Assignments .....	64
Issues .....	65
Project Earned Value .....	65
Project Earned Value and Issues - Monthly .....	66
Project Earned Value by Date Range .....	66
Project Plan Hierarchy .....	67
Project Status Report .....	68
Qualitative Risk Report .....	69
Risk Contingency Drawdown .....	70
Risk Exposure .....	70
Risk Scoring .....	71
S Curve .....	74
Weekly Schedule Performance .....	75
Resource Reports .....	76
Activity Resource Assignments .....	76
FTE (headcount) .....	76
Limit Line .....	77
Resource Code Assignments .....	78
Resource Role Associations .....	79
Resource Role Skill Sets .....	80
Resource Stacked Histogram .....	81
Role Code Assignments .....	81
<b>About Publication Services .....</b>	<b>82</b>
Working with Publication Services .....	83
Configuring Publication .....	84
Publishing P6 Data .....	85
Publication Services .....	85
Defining Publication Periods .....	86
Enabling Automatic Publishing of P6 Project Data .....	87
Enabling Automatic Publishing of P6 Global Data .....	88
Configuring Publication Service Settings for Projects .....	89
Creating Project Scheduled Services .....	90
Configuring Publication Service Settings for Baselines .....	91
Publishing P6 Project Data On Demand .....	91
Publishing P6 Global Data On Demand .....	92
Deleting Published P6 Project Data .....	92
Supported Parameters in P6 .....	93
Enumeration Parameters .....	94
Dynamic Parameters .....	97
Primitive Parameters .....	104
Allowing for Multiple Values Returned via a List .....	104
<b>About Table Auditing .....</b>	<b>105</b>
Configuring Audit Settings .....	105

